District Utility Program Meeting

District 2

October 26, 2023



THIS MEETING IS BEING RECORDED



WELCOME

Before we begin, let's have a brief safety moment.

In-Person Attendees

- Emergency Exits
- Tornado Shelter
- 911 Caller
- AED Location
- Restrooms

Virtual Attendees

 Unmute yourself or use your chat box if you are in an emergency situation.



AGENDA

- Introductions
- Utility Program Updates
- Construction Activities vs. Utility Conflicts
- Construction Projects Review
 - Outstanding 2023 Construction Projects
 - 2024 Construction Projects
 - 2025 Construction Projects
- Questions & Wrap Up



INTRODUCTIONS



INTRODUCE YOURSELF

Introduce yourself and share:

- Name
- Organization
- Role
- Favorite Pizza Topping

In-Person Attendees

Please go around the room and introduce yourself.

Virtual Attendees


Please type the information in the chat box.



UTILITY PROGRAM UPDATES



KEY OUTCOME



To improve utility coordination from Design through Construction.



IMPROVEMENT EMPHASIS

Communication during planning and construction

Improved utility
data collection
and plan
presentation

Construction schedule coordination



NDOT UTILITY SECTION



UTILITIES ORGANIZATION STRUCTURE





Katie Acevedo



Curt Yager



Don Horton



Rhett Robinson

Districts 1 & 8

Districts 2 & 3

District 4

Districts 5, 6, & 7




PROGRAM LEVEL UPDATES



ACCOMMODATION POLICY

- Sets forth guidelines & requirements for accommodating utility facilities within State Highway Property
- In process of completely revamping the policy

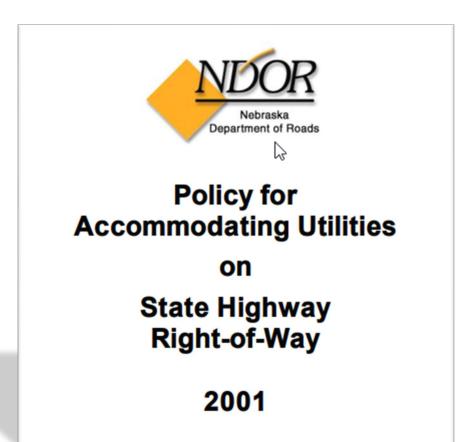



ACCOMMODATION POLICY

Current Step

Review & comment phase

Internal & FHWA concurrent review

Next Step

Implementation phase

Internal implementation & Stakeholder outreach



POLICY – KEY CHANGES

- Depth of bury by facility type
- Update casing requirements for steel pipelines
- Outlines NDOT utility coordination process
- Expand construction and maintenance requirements
- Identifies construction plan and 'As-Installed' plan requirements
- Addresses change in ownership and abandoned or out of service facilities
- Broadband chapter



PROJECT LEVEL UPDATES



CONFLICT ANALYSIS PROCESS

- Utility Company will perform Conflict Analysis
 - Review for conflicts with:
 - Final construction limits of construction, ROW, ditch grading
 - Temporary construction drives, access crossings, phasing
 - NDOT will review analysis and work with Utility Company
- If relocations are required, Utility Company will provide relocation information:
 - Scope of work
 - Detailed cost estimate
 - Schedule of relocation work



UTILITY QUESTIONNAIRE

- Receive via email from NDOT Utility Coordinator
- Action by Utility Company required:
 - Review and provide information for <u>existing facility locations</u>
 - Review existing locations for <u>construction conflicts</u>, both temporary and permanent conflicts
- Transmit responses and supporting documentation back to NDOT
- NDOT will track unresponsive utility companies & continue to follow up



RELOCATION PROCESS

- NDOT will review and provide comments on relocation plans and detailed cost estimate
 - Will be incorporated into the agreement
- Master (Blanket) Agreement or Utility Project Agreement
 - Only if relocation is reimbursable
- Letter of Authorization
 - Every relocation



2024 GOALS

- Implement Utility Accommodation Policy
- Identify utility conflicts early
- Coordinate utility relocations to be complete by construction start
- Professional development of coordinator staff
- 2024 District Utility Program Meetings October



ACTIVITIES VS. CONFLICTS

When we say	Think about
Access Crossings – Contractor ~Pipes or Temp. Bridge	Cranes and large equipment Impacts or proximity to overhead power Piling for temporary bridge
Shoo-flys – Traffic	In addition to access crossings Additional fill Impacts to pedestals, pull boxes, overhead power, etc.
Grade beam on pile	Cranes Impacts or proximity to overhead power
Over-excavation	Possibility on any project Most likely at culverts and locations of known muck



ACTIVITIES VS. CONFLICTS

When we say	Think about
Concrete Box Culverts	Sheet pile driven at wingwalls Impacts to buried lines Impacts or proximity to overhead power Temporary shoring on phased construction
Culvert Replacements - Phased construction	Potential for temporary shoring Need room (H & V) to construct end treatments
Culvert Replacements – Jacking	Large jacking pits - ~50'x100', not shown in plans Temporary excavation down to flowline to construct Need room (H & V) to construct end treatments



ACTIVITIES VS. CONFLICTS

When we say	Think about
Temporary Roads & Drives	Can require grading and ditch work Similar impacts to permanent construction
Guardrail	Posts can impact underground facilities
Sidewalk & ADA work	Pavement removal Shallow service lines
Curb Inlets	3 ft – 6 ft deep, in most cases Cast in place inlets require extra room for form work



CONSTRUCTION PROJECTS REVIEW



CONSTRUCTION PROJECTS REVIEW

District 2



OUTSTANDING CONSTRUCTION YEAR 2023

The following projects will likely not be completed in 2023



PARKER ST - FORT ST, OMAHA PROJECT NO.: NH-75-2(181); CONTROL NO.: 22647

- Project Length: 2.47
- Scope of Work:
 - Resurfacing
 - Pavement Repairs
 - Bridge Repair





PARKER ST - FORT ST, OMAHA PROJECT NO.: NH-75-2(181); CONTROL NO.: 22647

- Status: Under Construction
- Right-of-Way: Completed
- Traffic Impacts:
 - Phase Traffic Control
 - Local Detour
 - Overnight Alternate Route
- Letting Date: 4/6/2023
- Construction Timing: Active



PARKER ST - FORT ST, OMAHA PROJECT NO.: NH-75-2(181); CONTROL NO.: 22647

- Anticipated Utilities Impact:
 - Bridge Repair/Replace
- Anticipated Request from Utilities:
 - Coordination with NDOT
- Additional Information:
 - No K-Sheets Required
 - No Special Provisions Required
- Utilities Involved:
 - City of Omaha, Cox Communications, Metropolitan Utilities District, Omaha Public Power District



MURRAY - PLATTSMOUTH PROJECT NO.: NH-75-2(128); CONTROL NO.: 21209

- Project Length: 6.83
- Scope of Work:
 - Full Depth Pavement
 - Bridge Replacement
 - Grading





MURRAY - PLATTSMOUTH PROJECT NO.: NH-75-2(128); CONTROL NO.: 21209

- Status: Under Construction
- Right-of-Way: Completed
- Traffic Impacts:
 - Phase Traffic Control
 - Local Detour
- Letting Date: 11/19/2020
- Construction Timing: Active



MURRAY - PLATTSMOUTH PROJECT NO.: NH-75-2(128); CONTROL NO.: 21209

- Anticipated Utilities Impact:
 - Full Depth Pavement
 - Bridge Repair/Replace
 - Grading
- Anticipated Request from Utilities:
 - Coordination with NDOT
- Additional Information:
 - No K-Sheets Required
 - No Special Provisions Required
- Utilities Involved:
 - AT&T Communications, Black Hills Energy, Cass County RWD No.1, City of Plattsmouth, Enterprise Products LLC, Lumen(CenturyLink), Magellan Pipeline Company, Natural Gas Pipeline of America, Northern Natural Gas, Nebraska Public Power District, OneOk NGL Pipeline LLC, Omaha Public Power District, Pinpoint-Spiral Communications, Charter Communications(Spectrum), Cogent(T-Mobile-Sprint), Unite Private Networks, Zayo Group LLC



SCRIBNER NORTH & SOUTH PROJECT NO.: S-275-6(1053); CONTROL NO.: 32302A

- Project Length: 5.34
- Scope of Work:
 - Full Depth Pavement
 - Bridge Replacement
 - Grading





SCRIBNER NORTH & SOUTH PROJECT NO.: S-275-6(1053); CONTROL NO.: 32302A

- Status: Under Construction
- Right-of-Way: Completed
- Traffic Impacts:
 - Phase Traffic Control
 - Local Detour
- Letting Date: 9/30/2021
- Construction Timing: Active



SCRIBNER NORTH & SOUTH PROJECT NO.: S-275-6(1053); CONTROL NO.: 32302A

- Anticipated Utilities Impact:
 - Full Depth Pavement
 - Bridge Repair/Replace
 - Grading
- Anticipated Request from Utilities:
 - Coordination with NDOT
- Additional Information:
 - No K-Sheets Required
 - No Special Provisions Required
- Utilities Involved:
 - AT&T Communications, City of Scribner, Cuming County Public Power District, Great Plains Communications, Nebraska Public Power District



ACCIDENT INVESTIGATION SITES, OMAHA PROJECT NO.: HSIP-80-9(120); CONTROL NO.: 22828

- Project Length: 0
- Scope of Work:
 - ITS/Lighting





ACCIDENT INVESTIGATION SITES, OMAHA PROJECT NO.: HSIP-80-9(120); CONTROL NO.: 22828

- Status: Under Construction
- Right-of-Way: Completed
- Traffic Impacts:
 - Phase Traffic Control
- Letting Date: 6/15/2023
- Construction Timing: Active



ACCIDENT INVESTIGATION SITES, OMAHA PROJECT NO.: HSIP-80-9(120); CONTROL NO.: 22828

- Anticipated Utilities Impact:
 - No Impacts
- Anticipated Request from Utilities:
 - Coordination with NDOT
- Additional Information:
 - No K-Sheets Required
 - No Special Provisions Required
- Utilities Involved:
 - Bureau of Indian Affairs, Great Plains Communications, North Central Public Power District



CONSTRUCTION YEAR 2024

The following projects are anticipated to be let during 2024



US-75 WHITMORE NORTH, OMAHA PROJECT NO.: S-75-2(1081); CONTROL NO.: 22809

- Project Length: 1.77
- Scope of Work:
 - Resurfacing





US-75 WHITMORE NORTH, OMAHA PROJECT NO.: S-75-2(1081); CONTROL NO.: 22809

- Status: Under Construction
- Right-of-Way: Not Required
- Traffic Impacts:
 - Phase Traffic Control
- Letting Date: 8/24/2023
- Construction Timing: 5/1/2024




US-75 WHITMORE NORTH, OMAHA PROJECT NO.: S-75-2(1081); CONTROL NO.: 22809

- Anticipated Utilities Impact:
 - No Impacts
- Anticipated Request from Utilities:
 - Coordination with NDOT
- Additional Information:
 - No K-Sheets Required
 - No Special Provisions Required
- Utilities Involved:
 - City of Omaha, Cox Comm., Lumen (Century Link), Metropolitan Utility District, Omaha PPD, OneOK (Magellan), Ubiquity Nebraska LLC, Unite Private Networks, Verizon / MCI



N-370 - OMAHA PROJECT NO.: NH-STP-HSIP-50-2(135); CONTROL NO.: 22602

- Project Length: 5.45
- Scope of Work:
 - Resurfacing
 - Bridge Repair
 - Urban Reconstruction

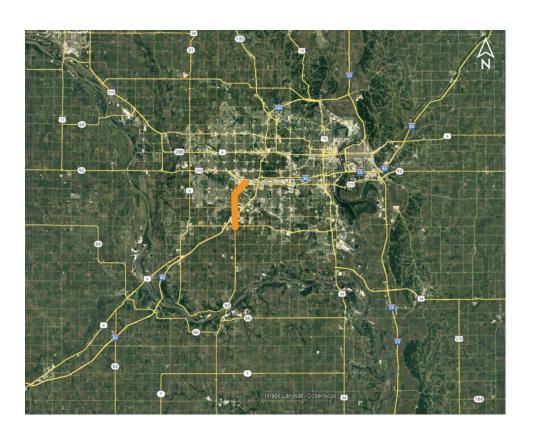



N-370 - OMAHA PROJECT NO.: NH-STP-HSIP-50-2(135); CONTROL NO.: 22602

- Status: Award Pending
- Right-of-Way: Completed
- Traffic Impacts:
 - Phase Traffic Control
 - Local Detour
 - Overnight Alternate Route
- Letting Date: 9/28/2023
- Construction Timing: 4/1/2024



N-370 - OMAHA PROJECT NO.: NH-STP-HSIP-50-2(135); CONTROL NO.: 22602

- Anticipated Utilities Impact:
 - Bridge Repair/Replacement
 - Guardrail
 - Full Depth Pavement
- Anticipated Request from Utilities:
 - Provide Existing Locations
 - Potholing TBD
 - Coordination with NDOT
- Additional Information:
 - K-Sheets Required
 - Special Provisions Required
- Utilities Involved:
 - AT&T Comm., Black Hills Energy, Cox Comm., Great Plains Comm., Lumen (Century Link), Metro Utility Dist., Nebraska PPD, Omaha PPD, OPK Networks (NebraskaLink), Sarpy County Public Works, Teleport Comm. America, Unite Private Networks, Verizon / MCI



DOUGLAS CO LINE - N-64 PROJECT NO.: NH-275-7(208); CONTROL NO.: 22844

- Project Length: 6.79
- Scope of Work:
 - Resurfacing
 - Pavement Repairs
 - Misc.





DOUGLAS CO LINE - N-64 PROJECT NO.: NH-275-7(208); CONTROL NO.: 22844

- Status: Award Pending
- Right-of-Way: Not Required
- Traffic Impacts:
 - Phase Traffic Control
 - Overnight Alternate Route
- Letting Date: 9/28/2023
- Construction Timing: 5/1/2024



DOUGLAS CO LINE - N-64 PROJECT NO.: NH-275-7(208); CONTROL NO.: 22844

- Anticipated Utilities Impact:
 - No Impacts
- Anticipated Request from Utilities:
 - Coordination with NDOT
- Additional Information:
 - No K-Sheets Required
 - No Special Provisions Required
- Utilities Involved:
 - Black Hills Energy, City of Valley, Cox Comm., Great Plains Comm., Lumen (Century Link), Metro Utility Dist., Omaha Public Power District, OneOK (Magellan), Unite Private Net., Verizon (MCI) Telecommunications



US-6/192ND ST INTERCHANGE, OMAHA PROJECT NO.: S-6-7(1060); CONTROL NO.: 22721

- Project Length: 0.96
- Scope of Work:
 - Urban Reconstruction
 - Culvert Extension/Replace
 - Full Depth Pavement





US-6/192ND ST INTERCHANGE, OMAHA PROJECT NO.: S-6-7(1060); CONTROL NO.: 22721

- Status: Preparing for Bid
- Right-of-Way: Completed
- Traffic Impacts:
 - Phase Traffic Control
 - Overnight Alternate Route
- Letting Date: 11/16/2023
- Construction Timing: 5/1/2024



US-6/192ND ST INTERCHANGE, OMAHA PROJECT NO.: S-6-7(1060); CONTROL NO.: 22721

- Anticipated Utilities Impact:
 - New Alignment
 - New ROW
 - Urban Reconstruction
- Anticipated Request from Utilities:
 - Provide Existing Locations
 - Coordination with NDOT
 - Potholing Required
- Additional Information:
 - K-Sheets Required
 - Special Provisions Required
- Utilities Involved:
 - AT&T Comm., City of Omaha, Cox Comm., Great Plains Comm., Lumen (Century Link), Metro Utility Dist., Omaha PPD, Unite Private Networks, Verizon / MCI



MAHONEY - N-370 PROJECT NO.: NH-HSIP-80-9(124); CONTROL NO.: 22847

- Project Length: 11.21
- Scope of Work:
 - Guardrail
 - Grading
 - Shoulder Work





MAHONEY - N-370 PROJECT NO.: NH-HSIP-80-9(124); CONTROL NO.: 22847

- Status: Award Pending
- Right-of-Way: Completed
- Traffic Impacts:
 - Phase Traffic Control
- Letting Date: 10/19/2023
- Construction Timing: 8/1/2024



MAHONEY - N-370 PROJECT NO.: NH-HSIP-80-9(124); CONTROL NO.: 22847

- Anticipated Utilities Impact:
 - Guardrail
 - Grading
 - Shoulder Work
- Anticipated Request from Utilities:
 - Coordination with NDOT
- Additional Information:
 - No K-Sheets Required
 - No Special Provisions Required
- Utilities Involved:
 - Black Hills Energy, Cox Comm., Omaha PPD, Unite Private Networks



NORTH BEND - FREMONT (RELINQUISHMENT) PROJECT NO.: S-30-6(1052); CONTROL NO.: 22473

- Project Length: 18.75
- Scope of Work:
 - Bridge Replacement
 - Resurfacing
 - Guardrail





NORTH BEND - FREMONT (RELINQUISHMENT) PROJECT NO.: S-30-6(1052); CONTROL NO.: 22473

- Status: Design
- Right-of-Way: Not Required
- Traffic Impacts:
 - Phase Traffic Control
 - Full Detour
- Letting Date: 2/29/2024
- Construction Timing: 5/20/2024



NORTH BEND - FREMONT (RELINQUISHMENT) PROJECT NO.: S-30-6(1052); CONTROL NO.: 22473

- Anticipated Utilities Impact:
 - Bridge Repair/Replacement
 - Guardrail
- Anticipated Request from Utilities:
 - Provide Existing Locations
 - Coordination with NDOT
- Additional Information:
 - No K-Sheets Required
 - Special Provisions TBD
- Utilities Involved:
 - Black Hills Energy, Charter Comm. (Spectrum), City of Fremont, City of Northbend, Great Plains Comm., Lumen (Century Link), Midstates Data Transport, Northern Natural Gas, Omaha PPD, Verizon / MCI



12TH ST - MO RIVER BR PAINT, OMAHA PROJECT NO.: NH-480-9(5); CONTROL NO.: 22703

- Project Length: 0.75
- Scope of Work:
 - Misc.





12TH ST - MO RIVER BR PAINT, OMAHA PROJECT NO.: NH-480-9(5); CONTROL NO.: 22703

- Status: Design
- Right-of-Way: Not Required
- Traffic Impacts:
 - Phase Traffic Control
 - Full Detour
- Letting Date: 4/11/2024
- Construction Timing: 5/1/2024



12TH ST - MO RIVER BR PAINT, OMAHA PROJECT NO.: NH-480-9(5); CONTROL NO.: 22703

- Anticipated Utilities Impact:
 - No Impacts
- Anticipated Request from Utilities:
 - Provide Existing Locations
- Additional Information:
 - No K-Sheets Required
 - No Special Provisions Required
- Utilities Involved:
 - City of Omaha, Cox Comm., Great Plains Comm., Lumen (Century Link), Metro Utility Dist., Omaha PPD, OPK Networks (NebraskaLink), Unite Private Networks



BAY ROAD BRIDGE PROJECT NO.: NH-34-7(136); CONTROL NO.: 22731A

- Project Length: 0
- Scope of Work:
 - Bridge Repair
 - Guardrail





BAY ROAD BRIDGE PROJECT NO.: NH-34-7(136); CONTROL NO.: 22731A

- Status: Preparing for Bid
- Right-of-Way: Not Required
- Traffic Impacts:
 - Phase Traffic Control
- Letting Date: 12/14/2023
- Construction Timing: 4/1/2024



BAY ROAD BRIDGE PROJECT NO.: NH-34-7(136); CONTROL NO.: 22731A

- Anticipated Utilities Impact:
 - No Impacts
- Anticipated Request from Utilities:
 - Provide Existing Locations
- Additional Information:
 - No K-Sheets Required
 - No Special Provisions Required
- Utilities Involved:
 - Northern Natural Gas, Omaha PPD, OneOK (Magellan), Pinpoint Comm. (Spiral Comm.), Windstream Comm., Zayo Group



I-480 MISSOURI RIVER BRIDGE PROJECT NO.: NH-480-9(11); CONTROL NO.: 22807

- Project Length: 0
- Scope of Work:
 - Bridge Repair
 - Pavement Repairs
 - Misc.





I-480 MISSOURI RIVER BRIDGE PROJECT NO.: NH-480-9(11); CONTROL NO.: 22807

- Status: Design
- Right-of-Way: Not Required
- Traffic Impacts:
 - Phase Traffic Control
- Letting Date: 4/11/2024
- Construction Timing:




I-480 MISSOURI RIVER BRIDGE PROJECT NO.: NH-480-9(11); CONTROL NO.: 22807

- Anticipated Utilities Impact:
 - Bridge Repair/Replace
 - No Impacts
- Anticipated Request from Utilities:
 - Provide Existing Locations
- Additional Information:
 - No K-Sheets Required
 - No Special Provisions Required
- Utilities Involved:
 - Cogent Comm. Inc. (T-Mobile, Sprint), Metro Utility Dist., Omaha PPD



SKYLINE DR - 168TH ST, OMAHA PROJECT NO.: NH-6-7(188); CONTROL NO.: 22811

- Project Length: 3.5
- Scope of Work:
 - Bridge Repair
 - Shoulder Work
 - Grading

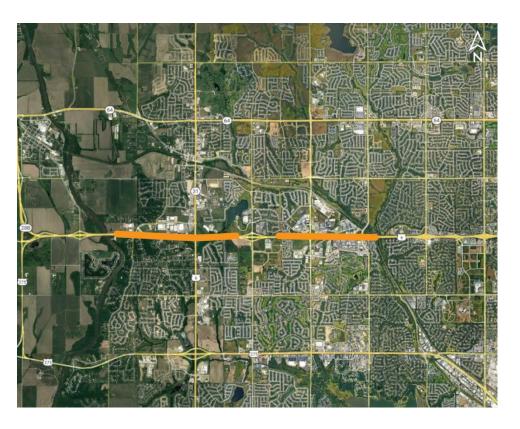



SKYLINE DR - 168TH ST, OMAHA PROJECT NO.: NH-6-7(188); CONTROL NO.: 22811

- Status: Design
- Right-of-Way: Not Required
- Traffic Impacts:
 - Phase Traffic Control
 - Full Detour
 - Overnight Alternate Route
- Letting Date: 2/29/2024
- Construction Timing: 5/1/2024




SKYLINE DR - 168TH ST, OMAHA PROJECT NO.: NH-6-7(188); CONTROL NO.: 22811

- Anticipated Utilities Impact:
 - Grading
 - Bridge Repair/Replace
 - Shoulder Work
- Anticipated Request from Utilities:
 - Provide Existing Locations
 - Coordination with NDOT
 - Locates
- Additional Information:
 - K-Sheets TBD
 - Special Provisions TBD
- Utilities Involved:
 - AT&T Comm., Cox Comm., Great Plains Comm., Lumen (Century Link), Metro Utility Dist., Omaha PPD, Pinpoint Comm. (Spiral Comm.), Verizon / MCI



60TH ST - 24TH ST, OMAHA PROJECT NO.: NH-80-9(118); CONTROL NO.: 22822

- Project Length: 2.36
- Scope of Work:
 - Resurfacing
 - Bridge Repair
 - Shoulder Work

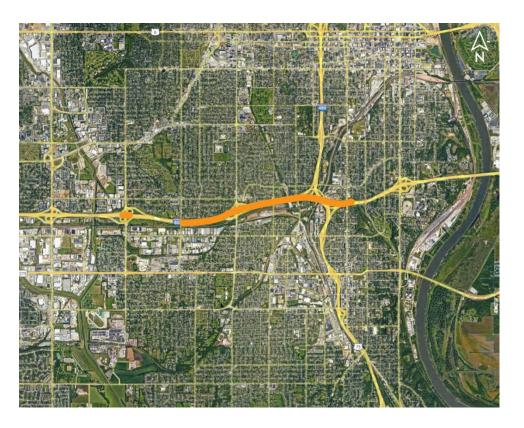



60TH ST - 24TH ST, OMAHA PROJECT NO.: NH-80-9(118); CONTROL NO.: 22822

- Status: Design
- Right-of-Way: Not Required
- Traffic Impacts:
 - Phase Traffic Control
 - Overnight Alternate Route
- Letting Date: 2/29/2024
- Construction Timing: 5/1/2024



60TH ST - 24TH ST, OMAHA PROJECT NO.: NH-80-9(118); CONTROL NO.: 22822

- Anticipated Utilities Impact:
 - No Impacts
- Anticipated Request from Utilities:
 - Provide Existing Locations
- Additional Information:
 - No K-Sheets Required
 - No Special Provisions Required
- Utilities Involved:
 - AT&T Comm., Cox Comm., Lumen (Century Link), Metro Utility Dist., Omaha PPD, Unite Private Networks



HARRISON ST - DODGE ST, OMAHA PROJECT NO.: NH-6-7(194); CONTROL NO.: 22861A

- Project Length: 5.04
- Scope of Work:
 - Pavement Repairs
 - Bridge Repair
 - Misc.





HARRISON ST - DODGE ST, OMAHA PROJECT NO.: NH-6-7(194); CONTROL NO.: 22861A

- Status: Design
- Right-of-Way: Not Required
- Traffic Impacts:
 - Phase Traffic Control
 - Overnight Alternate Route
- Letting Date: 2/29/2024
- Construction Timing: 4/1/2024




HARRISON ST - DODGE ST, OMAHA PROJECT NO.: NH-6-7(194); CONTROL NO.: 22861A

- Anticipated Utilities Impact:
 - No Impacts
- Anticipated Request from Utilities:
 - Provide Existing Locations
- Additional Information:
 - No K-Sheets Required
 - No Special Provisions Required
- Utilities Involved:
 - AT&T Comm., Black Hills Energy, City of Gretna, Cox Comm., Great Plains Comm., Lumen (Century Link), Omaha PPD, Papio-Missouri NRD, Unite Private Networks, Verizon / MCI



US-275/N-92 CULVERT PROJECT NO.: MISC-275-7(1047); CONTROL NO.: 22892

- Project Length: 0
- Scope of Work:
 - Culvert Extension/Replace
 - Shoulder Work
 - Grading

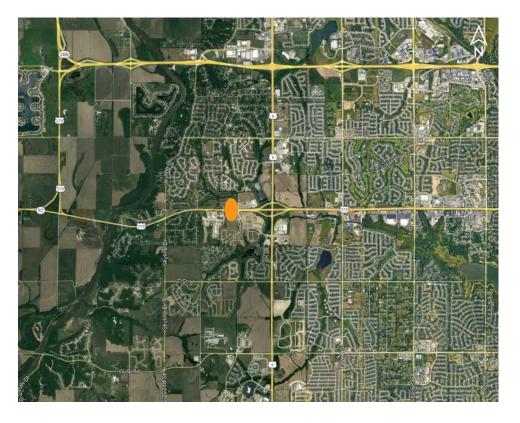



US-275/N-92 CULVERT PROJECT NO.: MISC-275-7(1047); CONTROL NO.: 22892

- Status: Design
- Right-of-Way: Not Required
- Traffic Impacts:
 - Phase Traffic Control
- Letting Date: 7/25/2024
- Construction Timing: 3/1/2024




US-275/N-92 CULVERT PROJECT NO.: MISC-275-7(1047); CONTROL NO.: 22892

- Anticipated Utilities Impact:
 - Culvert Extension/Replacement
- Anticipated Request from Utilities:
 - Provide Existing Locations
 - Potholing TBD
- Additional Information:
 - No K-Sheets Required
 - Special Provisions TBD
- Utilities Involved:
 - Cox Comm., Great Plains Comm., Lumen (Century Link), Metro Utility Dist., Omaha PPD



US-34 TO I-80, OMAHA PROJECT NO.: NH-75-2(188); CONTROL NO.: 22859

- Project Length: 8.07
- Scope of Work:
 - Pavement Repairs
 - Misc.

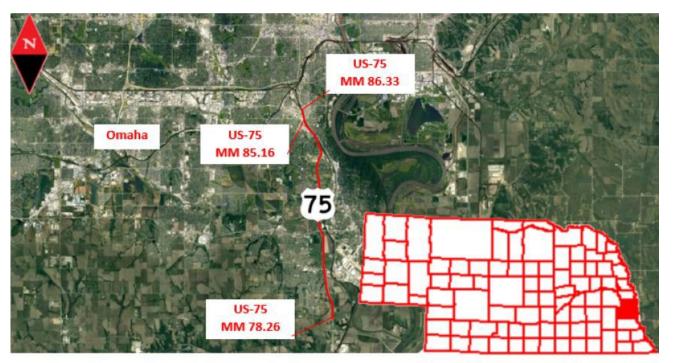

SARPY and DOUGLAS COUNTIES



US-34 TO I-80, OMAHA PROJECT NO.: NH-75-2(188); CONTROL NO.: 22859

- Status: Design
- Right-of-Way: Not Required
- Traffic Impacts:
 - Phase Traffic Control
 - Overnight Alternate Route
- Letting Date: 6/20/2024
- Construction Timing: 11/1/2024




US-34 TO I-80, OMAHA PROJECT NO.: NH-75-2(188); CONTROL NO.: 22859

- Anticipated Utilities Impact:
 - No Impacts
- Anticipated Request from Utilities:
 - Provide Existing Locations
- Additional Information:
 - No K-Sheets Required
 - No Special Provisions Required
- Utilities Involved:
 - AT&T Comm., Black Hills Energy, City of Bellevue, City of Omaha, Cogent Comm. Inc. (T-Mobile, Sprint), Cox Comm., Fastwyre Broadband (ABB), Great Plains Comm., Lumen (Century Link), Metro Utility Dist., Northern Natural Gas, Omaha PPD, Unite Private Networks, Verizon / MCI, Windstream Comm., Zayo Group



MURRAY WEST PROJECT NO.: STP-4-7(111); CONTROL NO.: 22625

- Project Length: 5.44
- Scope of Work:
 - Pavement Repairs
 - Misc.

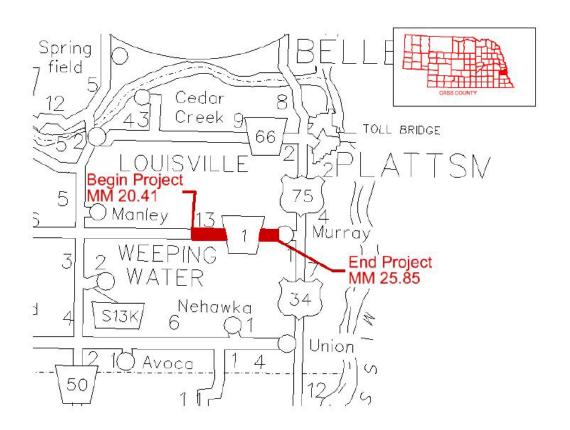



MURRAY WEST PROJECT NO.: STP-4-7(111); CONTROL NO.: 22625

- Status: Design
- Right-of-Way: Not Required
- Traffic Impacts:
 - Phase Traffic Control
 - Local Detour
- Letting Date: 2/29/2024
- Construction Timing: 4/1/2024



MURRAY WEST PROJECT NO.: STP-4-7(111); CONTROL NO.: 22625

- Anticipated Utilities Impact:
 - No Impacts
- Anticipated Request from Utilities:
 - Provide Existing Locations
- Additional Information:
 - No K-Sheets Required
 - No Special Provisions Required
- Utilities Involved:
 - AT&T Comm., Black Hills Energy, Cass County RWD 1, Kinder Morgan, Nebraska PPD, Omaha PPD, OneOK (Magellan), Otoe County RWD 3, Unite Private Networks, Village of Murray, Windstream Comm.



BANCROFT ST - DEWEY ST, OMAHA PROJECT NO.: NH-480-9(12); CONTROL NO.: 22824

- Project Length: 2.35
- Scope of Work:
 - Misc.





BANCROFT ST - DEWEY ST, OMAHA PROJECT NO.: NH-480-9(12); CONTROL NO.: 22824

- Status: Award Pending
- Right-of-Way: Not Required
- Traffic Impacts:
 - Phase Traffic Control
 - Overnight Alternate Route
- Letting Date: 8/24/2023
- Construction Timing: 3/18/2024



BANCROFT ST - DEWEY ST, OMAHA PROJECT NO.: NH-480-9(12); CONTROL NO.: 22824

- Anticipated Utilities Impact:
 - No Impacts
- Anticipated Request from Utilities:
 - Provide Existing Locations
- Additional Information:
 - No K-Sheets Required
 - No Special Provisions Required
- Utilities Involved:
 - AT&T Comm., City of Omaha, Cogent Comm. Inc. (T-Mobile, Sprint), Cox Comm., Great Plains Comm., Lumen (Century Link), Metro Utility Dist., Omaha PPD, Unite Private Networks, Verizon / MCI, Windstream Comm.



I-80/I-680 INTERCHANGE - Q ST (WB), OMAHA PROJECT NO.: NH-80-9(207); CONTROL NO.: 22887

- Project Length: 1.79
- Scope of Work:
 - Misc.





I-80/I-680 INTERCHANGE - Q ST (WB), OMAHA PROJECT NO.: NH-80-9(207); CONTROL NO.: 22887

- Status: Design
- Right-of-Way: Not Required
- Traffic Impacts:
 - Phase Traffic Control
 - Overnight Alternate Route
- Letting Date: 2/29/2024
- Construction Timing: 11/1/2024



I-80/I-680 INTERCHANGE - Q ST (WB), OMAHA PROJECT NO.: NH-80-9(207); CONTROL NO.: 22887

- Anticipated Utilities Impact:
 - No Impacts
- Anticipated Request from Utilities:
 - Provide Existing Locations
- Additional Information:
 - No K-Sheets Required
 - No Special Provisions Required
- Utilities Involved:
 - AT&T Comm., City of Omaha, Cox Comm., Great Plains Comm., Lumen (Century Link), Metro Utility Dist., Midwest Fiber Networks, Omaha PPD, OPTK Networks (NebraskaLink), Unite Private Networks, Verizon / MCI



13TH ST WEST, OMAHA PROJECT NO.: NH-80-9(119); CONTROL NO.: 22823

- Project Length: 0.91
- Scope of Work:
 - Misc.





13TH ST WEST, OMAHA PROJECT NO.: NH-80-9(119); CONTROL NO.: 22823

- Status: Award Pending
- Right-of-Way: Not Required
- Traffic Impacts:
 - Phase Traffic Control
 - Overnight Alternate Route
- Letting Date: 8/24/2023
- Construction Timing: 11/1/2023



13TH ST WEST, OMAHA PROJECT NO.: NH-80-9(119); CONTROL NO.: 22823

- Anticipated Utilities Impact:
 - No Impacts
- Anticipated Request from Utilities:
 - Provide Existing Locations
- Additional Information:
 - No K-Sheets Required
 - No Special Provisions Required
- Utilities Involved:
 - AT&T Comm., City of Omaha, Cox Comm., Great Plains Comm., Lumen (Century Link), Metro Utility Dist., Omaha PPD, Unite Private Networks, Verizon / MCI, Windstream Comm., Zayo Group



CONSTRUCTION YEAR 2025

The following projects are anticipated to be let during 2025



UNION - MURRAY (MS) PROJECT NO.: NH-34-7(129); CONTROL NO.: 22543

- Project Length: 7.01
- Scope of Work:
 - Resurfacing
 - Shoulder Work
 - Bridge Repair





UNION - MURRAY (MS) PROJECT NO.: NH-34-7(129); CONTROL NO.: 22543

- Status: Design
- Right-of-Way: In Progress
- Traffic Impacts:
 - Phase Traffic Control
- Letting Date: 8/29/2024
- Construction Timing: 5/1/2025



UNION - MURRAY (MS) PROJECT NO.: NH-34-7(129); CONTROL NO.: 22543

- Anticipated Utilities Impact:
 - Shoulder Work
 - Grading
 - Bridge Repair/Replace
- Anticipated Request from Utilities:
 - Provide Existing Locations
 - Potholing TBD
 - Coordination with NDOT
- Additional Information:
 - K-Sheets TBD
 - Special Provisions TBD
- Utilities Involved:
 - Cass County RWD, Lumen (CenturyLink), Nebraska PPD, Nustar Pipeline, Omaha PPD, OneOK (Magellan), Village of Murray, Village of Union, Windstream Comm., Zayo Group



N-1 - LOUISVILLE (MS) PROJECT NO.: STP-50-2(139); CONTROL NO.: 22803

- Project Length: 7.37
- Scope of Work:
 - Resurfacing
 - Bridge Replacement
 - Full Depth Pavement





N-1 - LOUISVILLE (MS) PROJECT NO.: STP-50-2(139); CONTROL NO.: 22803

- Status: Design
- Right-of-Way: In Progress
- Traffic Impacts:
 - Phase Traffic Control
- Letting Date: 8/29/2024
- Construction Timing: 4/1/2025



N-1 - LOUISVILLE (MS) PROJECT NO.: STP-50-2(139); CONTROL NO.: 22803

- Anticipated Utilities Impact:
 - Bridge Repair/Replacement
 - Full Depth Pavement
- Anticipated Request from Utilities:
 - Provide Existing Locations
 - Coordination with NDOT
 - Locates
- Additional Information:
 - K-Sheets TBD
 - Special Provisions TBD
- Utilities Involved:
 - Black Hills Energy, Charter Comm. (Spectrum), City of Louisville, Great Plains Comm., Kinder Morgan, Northern Natural Gas, Omaha PPD, OPTK Networks (NebraskaLink), Otoe County RWD 3, Unite Private Networks, Verizon / MCI, Village of Manley, Windstream Comm., Zayo Group



N-50/N-31 INTERSECTION PROJECT NO.: STP-50-2(140); CONTROL NO.: 22805

- Project Length: 0
- Scope of Work:
 - Pavement Repairs
 - Grading
 - Full Depth Pavement





N-50/N-31 INTERSECTION PROJECT NO.: STP-50-2(140); CONTROL NO.: 22805

- Status: Design
- Right-of-Way: None Required
- Traffic Impacts:
 - Phase Traffic Control
- Letting Date: 8/29/2024
- Construction Timing: 5/1/2025



N-50/N-31 INTERSECTION PROJECT NO.: STP-50-2(140); CONTROL NO.: 22805

- Anticipated Utilities Impact:
 - Turn Lane Add/Adjust
 - Full Depth Pavement
- Anticipated Request from Utilities:
 - Provide Existing Locations
 - Coordination with NDOT
- Additional Information:
 - K-Sheets TBD
 - Special Provisions Required
- Utilities Involved:
 - Charter Comm. (Spectrum), City of Louisville, Lumen (CenturyLink), Omaha PPD, OPTK Networks (NebraskaLink), Unite Private Networks, Verizon / MCI, Windstream Comm., Zayo Group



S PAPILLION CR & W PAPILLION CR BRIDGES PROJECT NO.: NH-80-9(115); CONTROL NO.: 22810

- Project Length: 1.75
- Scope of Work:
 - Bridge Repair
 - Guardrail
 - Grading





S PAPILLION CR & W PAPILLION CR BRIDGES PROJECT NO.: NH-80-9(115); CONTROL NO.: 22810

- Status: Design
- Right-of-Way: Not Required
- Traffic Impacts:
 - Phase Traffic Control
- Letting Date: 8/29/2024
- Construction Timing: 5/1/2025



S PAPILLION CR & W PAPILLION CR BRIDGES PROJECT NO.: NH-80-9(115); CONTROL NO.: 22810

- Anticipated Utilities Impact:
 - Bridge Repair/Replacement
 - Guardrail
 - Grading
- Anticipated Request from Utilities:
 - Provide Existing Locations
 - Coordination with NDOT
- Additional Information:
 - No K-Sheets Required
 - No Special Provisions Required
- Utilities Involved:
 - Cox Comm., Lumen (Century Link), Metropolitan Utility District



156TH ST - 132ND ST, OMAHA PROJECT NO.: NH-6-7(189); CONTROL NO.: 22812

- Project Length: 2.62
- Scope of Work:
 - Bridge Repair
 - Shoulder Work
 - Grading





156TH ST - 132ND ST, OMAHA PROJECT NO.: NH-6-7(189); CONTROL NO.: 22812

- Status: Design
- Right-of-Way: Completed
- Traffic Impacts:
 - Phase Traffic Control
 - Overnight Alternate Route
 - Full Detour
- Letting Date: 8/29/2024
- Construction Timing: 5/1/2025



156TH ST - 132ND ST, OMAHA PROJECT NO.: NH-6-7(189); CONTROL NO.: 22812

- Anticipated Utilities Impact:
 - Grading
 - Shoulder Work
- Anticipated Request from Utilities:
 - Provide Existing Locations
 - Coordination with NDOT
- Additional Information:
 - No K-Sheets Required
 - No Special Provisions Required
- Utilities Involved:
 - AT&T Comm., City of Omaha, Cox Comm., Lumen (Century Link), Metropolitan Utility District, Omaha PPD, Pinpoint Comm. (Spiral Comm.), Unite Private Networks, Verizon / MCI, Windstream Comm.



N-64 - L28B PROJECT NO.: NH-HSIP-275-7(207); CONTROL NO.: 22843

- Project Length: 7.66
- Scope of Work:
 - Pavement Repairs
 - Shoulder Work
 - Bridge Repair





N-64 - L28B PROJECT NO.: NH-HSIP-275-7(207); CONTROL NO.: 22843

- Status: Design
- Right-of-Way: Not Required
- Traffic Impacts:
 - Phase Traffic Control
- Letting Date: 8/29/2024
- Construction Timing: 5/1/2025




N-64 - L28B PROJECT NO.: NH-HSIP-275-7(207); CONTROL NO.: 22843

- Anticipated Utilities Impact:
 - No Impacts
- Anticipated Request from Utilities:
 - Provide Existing Locations
- Additional Information:
 - No K-Sheets Required
 - No Special Provisions Required
- Utilities Involved:
 - Black Hills Energy, City of Valley, Cox Comm., Great Plains Comm., Lumen (Century Link), Omaha PPD, Unite Private Networks, Verizon / MCI



US-75 & N 48TH ST PROJECT NO.: NH-75-2(191); CONTROL NO.: 22874

- Project Length: 0.13
- Scope of Work:
 - Culvert Extension/Replace
 - Grading
 - Misc.

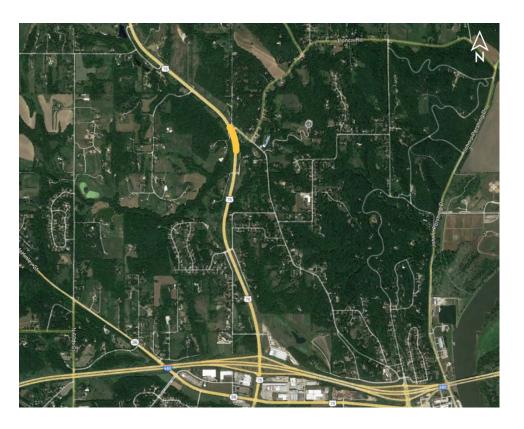



US-75 & N 48TH ST PROJECT NO.: NH-75-2(191); CONTROL NO.: 22874

- Status: Design
- Right-of-Way: In Progress
- Traffic Impacts:
 - Phase Traffic Control
- Letting Date: 8/29/2024
- Construction Timing: 9/1/2025



US-75 & N 48TH ST PROJECT NO.: NH-75-2(191); CONTROL NO.: 22874

- Anticipated Utilities Impact:
 - Culvert Extension/Replacement
 - Grading
 - Guardrail
- Anticipated Request from Utilities:
 - Provide Existing Locations
 - Coordination with NDOT
- Additional Information:
 - No K-Sheets Required
 - Special Provisions Required
- Utilities Involved:
 - Cox Comm., Lumen (Century Link), Metropolitan Utility District, Omaha PPD, Washington Co. RWD #1



DISTRICT 2-B HIGH MAST TOWER REPLACEMENT PROJECT NO.: STP-680-9(44); CONTROL NO.: 22899

- Project Length: 0
- Scope of Work:
 - ITS/Lighting
 - Grading
 - Misc.





DISTRICT 2-B HIGH MAST TOWER REPLACEMENT PROJECT NO.: STP-680-9(44); CONTROL NO.: 22899

- Status: Design
- Right-of-Way: Not Required
- Traffic Impacts:
 - Phase Traffic Control
- Letting Date: 8/29/2024
- Construction Timing: 5/1/2025




DISTRICT 2-B HIGH MAST TOWER REPLACEMENT PROJECT NO.: STP-680-9(44); CONTROL NO.: 22899

- Anticipated Utilities Impact:
 - Lighting
- Anticipated Request from Utilities:
 - Provide Existing Locations
 - Potholing TBD
- Additional Information:
 - No K-Sheets Required
 - Special Provisions TBD
- Utilities Involved:
 - AT&T Comm., City of Omaha, Cox Comm., Great Plains Comm., Lumen (Century Link), Metropolitan Utility District, Omaha PPD, OneOK (Magellan), Unite Private Networks, Verizon / MCI, Windstream Comm.



DISTRICT 2-C HIGH MAST TOWER REPLACEMENT PROJECT NO.: STP-680-9(43); CONTROL NO.: 22900

- Project Length: 0
- Scope of Work:
 - ITS/Lighting
 - Grading
 - Misc.

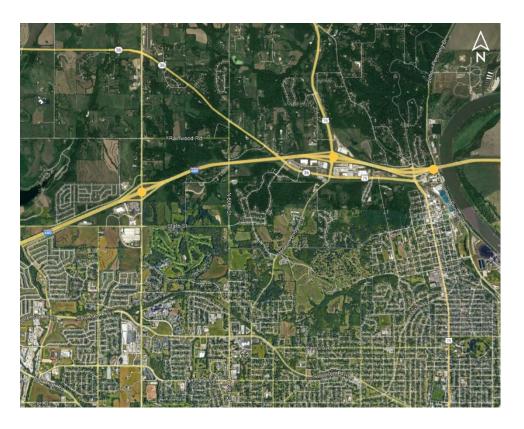



DISTRICT 2-C HIGH MAST TOWER REPLACEMENT PROJECT NO.: STP-680-9(43); CONTROL NO.: 22900

- Status: Design
- Right-of-Way: Not Required
- Traffic Impacts:
 - Phase Traffic Control
- Letting Date: 8/29/2024
- Construction Timing: 5/1/2025




DISTRICT 2-C HIGH MAST TOWER REPLACEMENT PROJECT NO.: STP-680-9(43); CONTROL NO.: 22900

- Anticipated Utilities Impact:
 - Lighting
- Anticipated Request from Utilities:
 - Provide Existing Locations
 - Potholing TBD
- Additional Information:
 - No K-Sheets Required
 - Special Provisions TBD
- Utilities Involved:
 - City of Omaha, Cox Comm., Fastwyre Broadband (ABB), Great Plains Comm., Lumen (Century Link), Metropolitan Utility District, Omaha PPD, OneOK (Magellan), Unite Private Networks, Verizon / MCI



N-66 CONNECTION IN LOUISVILLE PROJECT NO.: STP-66-7(119); CONTROL NO.: 22795

- Project Length: 0.54
- Scope of Work:
 - Resurfacing
 - Full Depth Pavement
 - Misc.

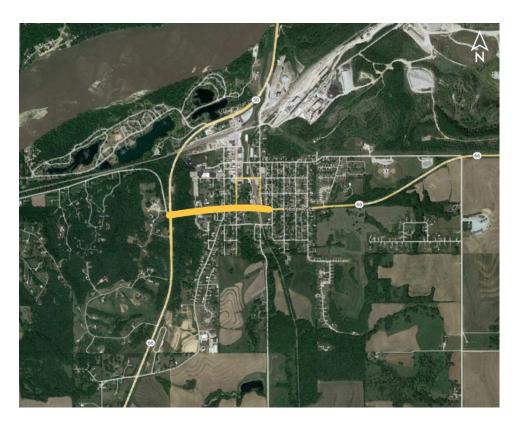



N-66 CONNECTION IN LOUISVILLE PROJECT NO.: STP-66-7(119); CONTROL NO.: 22795

- Status: Design
- Right-of-Way: In Progress
- Traffic Impacts:
 - Phase Traffic Control
 - Full Detour
- Letting Date: 8/28/2025
- Construction Timing: 10/1/2025



N-66 CONNECTION IN LOUISVILLE PROJECT NO.: STP-66-7(119); CONTROL NO.: 22795

- Anticipated Utilities Impact:
 - Bridge Repair/Replace
 - Grading
- Anticipated Request from Utilities:
 - Utilities Workshop
 - Provide Existing Locations
 - Coordination with NDOT
- Additional Information:
 - K-Sheets Required
 - Special Provisions Required
- Utilities Involved:
 - Black Hills Energy, Charter Comm. (Spectrum), City of Louisville, Omaha PPD, OPTK Networks (NebraskaLink), Unite Private Networks, Windstream Comm.



PLATTE RIVER - MILLARD EAST PROJECT NO.: NH-80-9(139); CONTROL NO.: 22919

- Project Length: 14.9
- Scope of Work:





PLATTE RIVER - MILLARD EAST PROJECT NO.: NH-80-9(139); CONTROL NO.: 22919

- Status: Design
- Right-of-Way: Not Required
- Traffic Impacts:
 - Phase Traffic Control
 - Overnight Alternate Route
- Letting Date: 7/24/2025
- Construction Timing: 5/1/2026




PLATTE RIVER - MILLARD EAST PROJECT NO.: NH-80-9(139); CONTROL NO.: 22919

- Anticipated Utilities Impact:
 - No Impacts
- Anticipated Request from Utilities:
 - Provide Existing Locations
- Additional Information:
 - No K-Sheets Required
 - No Special Provisions Required
- Utilities Involved:
 - AT&T Comm., Black Hills Energy, Charter Comm. (Spectrum), City of Gretna, City of La Vista, City of Lincoln, City of Omaha, Cox Comm., Great Plains Comm., Lumen (Century Link), Metropolitan Utility District, Northern Natural Gas, Omaha PPD, Sarpy County Sewer, Unite Private Networks, Verizon / MCI, Zayo Group



FORT ST - MISSOURI RIVER PROJECT NO.: NH-680-9(55); CONTROL NO.: 22886

- Project Length: 7.47
- Scope of Work:
 - Misc.

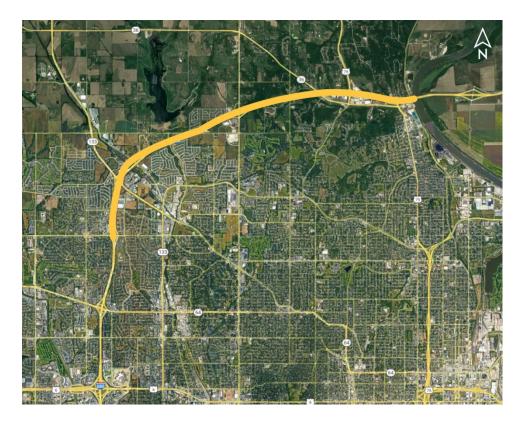



FORT ST - MISSOURI RIVER PROJECT NO.: NH-680-9(55); CONTROL NO.: 22886

- Status: Planning
- Right-of-Way: Not Required
- Traffic Impacts:
 - Phase Traffic Control
 - Overnight Alternate Route
- Letting Date: 8/15/2024
- Construction Timing: 11/1/2025



FORT ST - MISSOURI RIVER PROJECT NO.: NH-680-9(55); CONTROL NO.: 22886

- Anticipated Utilities Impact:
 - No Impacts
- Anticipated Request from Utilities:
 - Provide Existing Locations
- Additional Information:
 - No K-Sheets Required
 - No Special Provisions Required
- Utilities Involved:
 - AT&T Communications, City of Omaha, Cox Communications, Fastwyre, Great Plains Communications, Lumen(CenturyLink), Magellan Mistreams Partners LP, Metropolitan Utilities District, Nebraska Link/OPTK Networks, Omaha Public Power District, Unite Private Networks, Verizon/MCI Telecommunications, Windstream Communications, Zayo Group



SCRIBNER RELINQUISHMENT PROJECT NO.: S-275-6(1058); CONTROL NO.: 32302F

- Project Length: 1.38
- Scope of Work:
 - Resurfacing
 - Pavement Repairs
 - Shoulder Work





SCRIBNER RELINQUISHMENT PROJECT NO.: S-275-6(1058); CONTROL NO.: 32302F

- Status: Design
- Right-of-Way: Not Required
- Traffic Impacts:
 - Phase Traffic Control
- Letting Date: 8/29/2024
- Construction Timing: 4/1/2025



SCRIBNER RELINQUISHMENT PROJECT NO.: S-275-6(1058); CONTROL NO.: 32302F

- Anticipated Utilities Impact:
 - Shoulder Work
- Anticipated Request from Utilities:
 - Provide Existing Locations
 - Coordination with NDOT
- Additional Information:
 - No K-Sheets Required
 - No Special Provisions Required
- Utilities Involved:
 - City of Scribner, Cuming County PPD, Great Plains Comm.



QUESTIONS & WRAP UP



ANY FINAL QUESTIONS?


Ask them now!

If you have questions after this meeting, or would like to view more detailed project maps, please reach out to your utility coordinator.



HAVE A QUESTION ABOUT A PROJECT YOUR UTILITY IS INVOLVED IN?

Contact your district's utility coordinator!

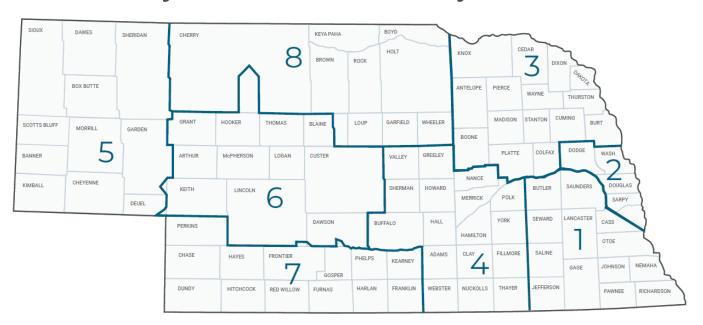

Utility Coordinators

District 4

Don Horton 402-479-4732 don.horton@nebraska.gov

Districts 5, 6, & 7

Rhett Robinson 402-479-3552 rhett.robinson@nebraska.gov

Districts 1 & 8

Katie Acevedo 402-479-3999 katie.acevedo@nebraska.gov

Districts 2 & 3

Curt Yager 402-479-4425 curt.yager@nebraska.gov

Utility Engineer

Dave Hansen 402-479-4459 david.t.hansen@nebraska.gov

Professional Engineer

Kathy Fischer 402-479-4446 katharine.fischer@nebraska.gov

Utilities Section

PO Box 94759 Lincoln, NE 68509-4759 NDOT.RD-Utilities@nebraska.gov



WE NEED YOUR FEEDBACK

Your valuable feedback helps these meetings – and NDOT's utility coordination program – be better.

Use your phone's camera to scan this QR code or use our paper survey.





VISIT OUR WEBSITE

Visit NDOT.info/utility for more information on:

- Utility accommodation
- Permitting
- Coordination
- Project information
- Reimbursements
- Additional information



Thank You

