

Nebraska State Highway Commission West Beltway Update

September 22, 2023

NEBRASKA

Good Life. Great Journey.


DEPARTMENT OF TRANSPORTATION

AGENDA





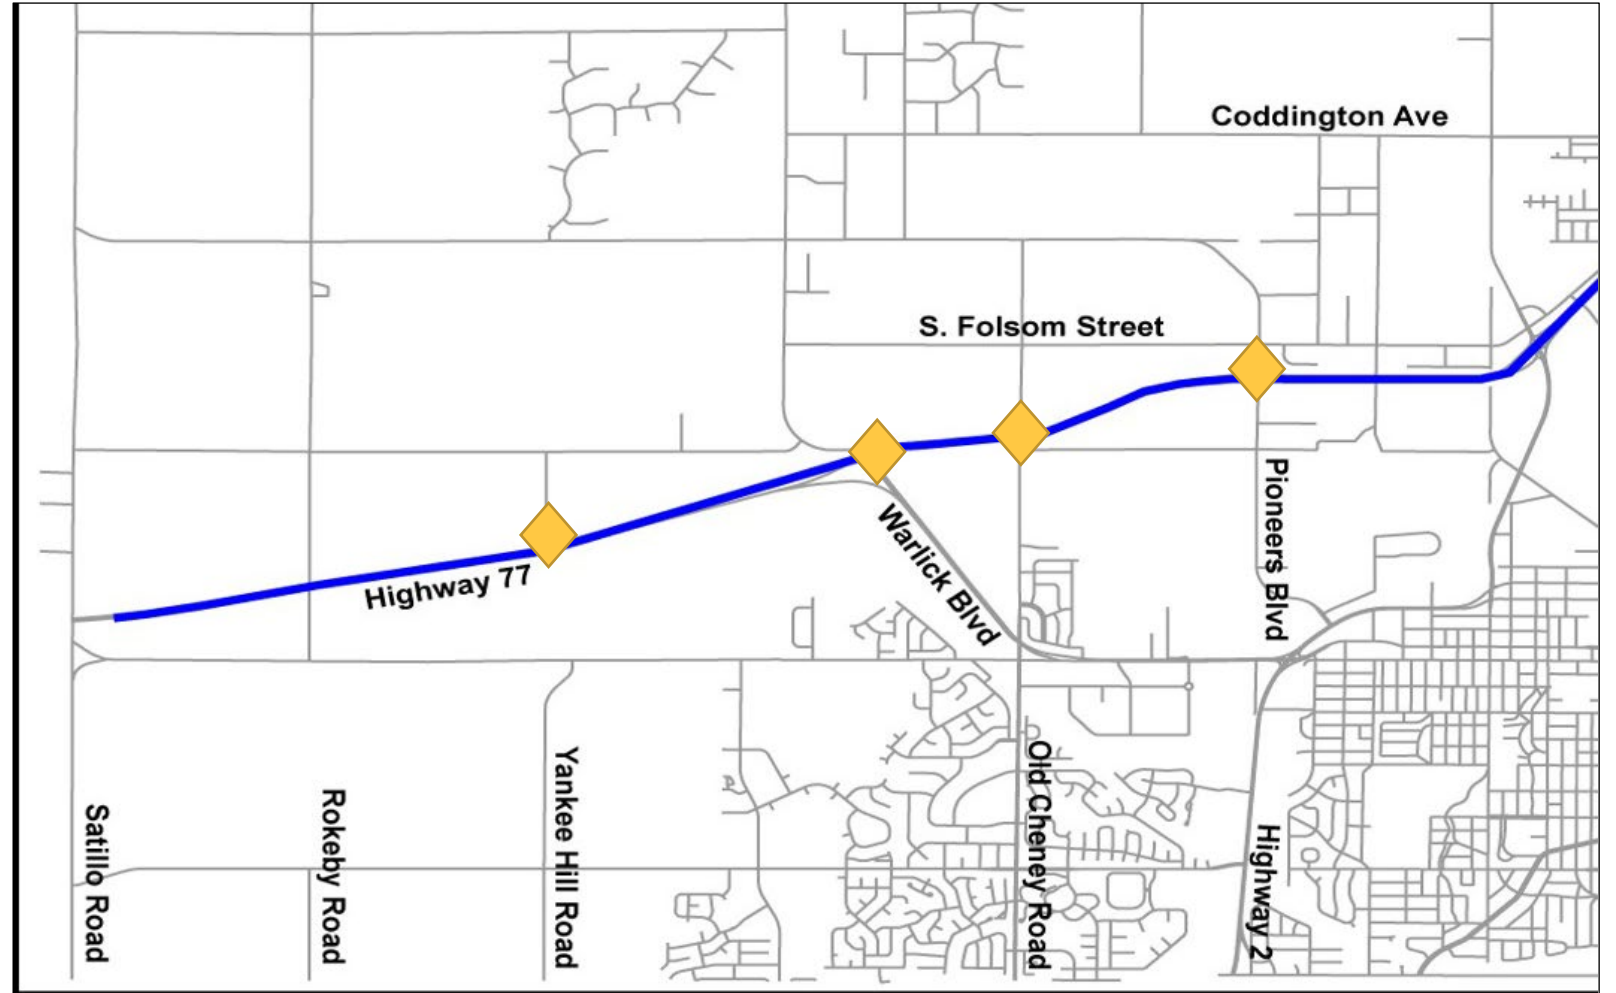


- Project Overview
- Range of Options
- Traffic Analysis
- Current Activities
- Schedule – Cost - Stakeholders




PROJECT OVERVIEW



RANGE OF OPTIONS

	1 (No Build)	2	3	4	5
Warlick Blvd	 SIGNAL	 INTERCHANGE	 INTERCHANGE	 INTERCHANGE	 INTERCHANGE
Old Cheney Rd	 SIGNAL	 CLOSED	 OVERPASS	 CLOSED	 OVERPASS
Pioneers Blvd	 SIGNAL	 INTERCHANGE	 INTERCHANGE	 OVERPASS	 OVERPASS

TRAFFIC LEVEL OF SERVICE

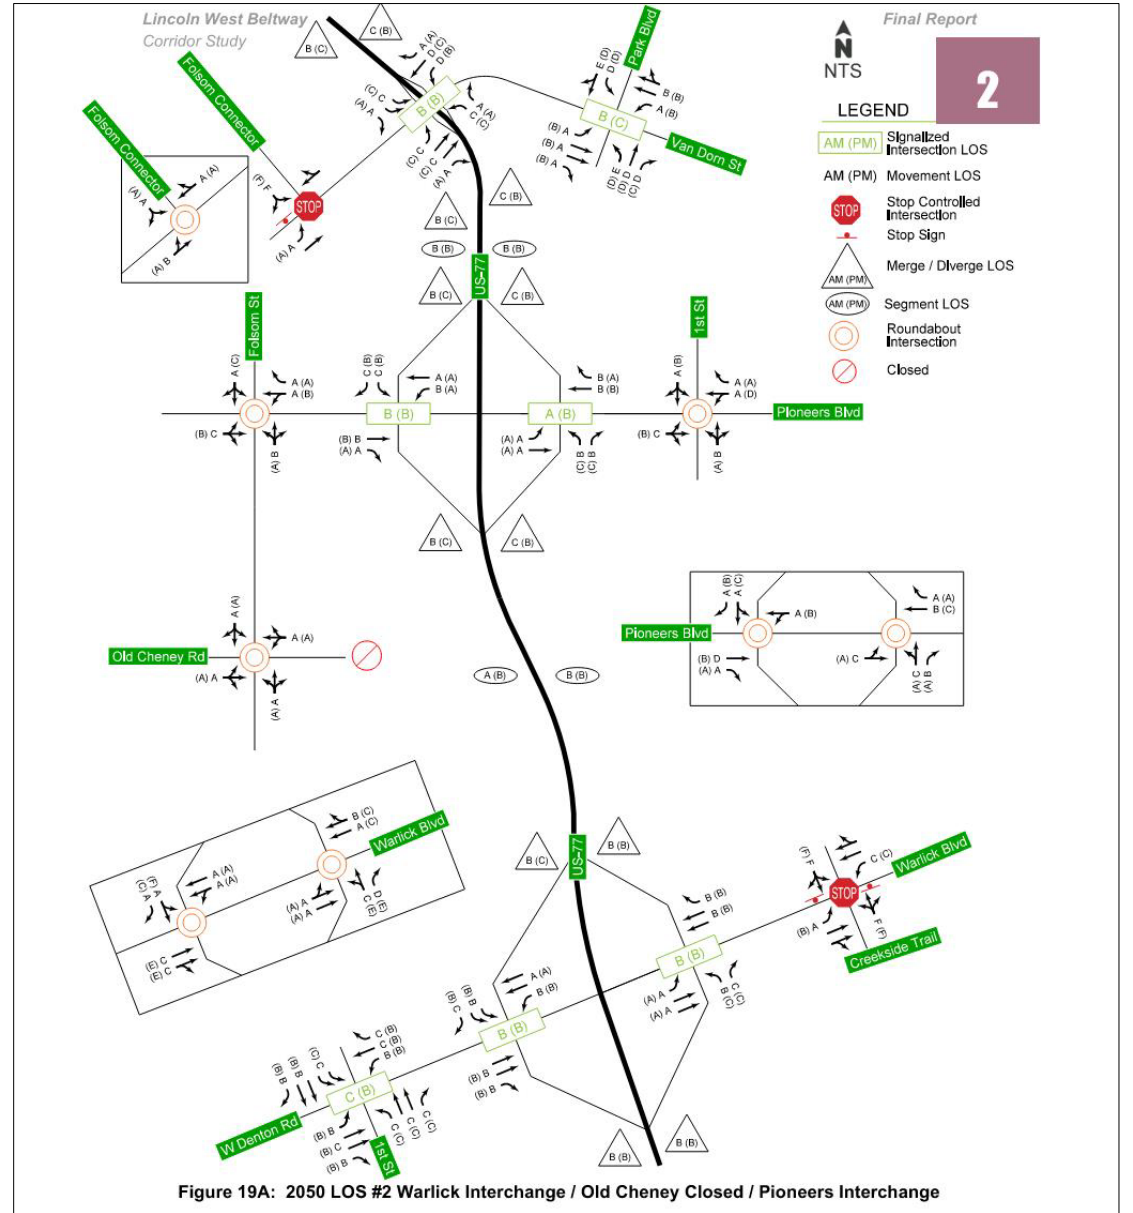

CURRENT ACTIVITIES

- ✓ Completed updated Corridor Study – October 2022
- ✓ Alternative Layouts with cost estimate – October 2023
- ✓ Completing survey
- ✓ Begun NEPA document re-evaluation
- ✓ Anticipate a public information meeting in early 2024



SCHEDULE – COST - STAKEHOLDERS

- NDOT program book has West Beltway listed in the 5-year plan between 2025 thru 2029
- Current program estimate is \$ 34.8 million based upon a 10% design level.
- NDOT design / environmental team is meeting quarterly with the City of Lincoln and Lancaster County.
- Key stakeholder groups will be formed for updates beyond typical public communication. These include local businesses | local & regional elected officials | Friend of Wilderness Park | Bicycle Groups

Questions?

Steve McCullough, PE

Assistant Roadway Design Engineer

Steve.McCullough@nebraska.gov
