Unforeseen Circumstances

L-62A North

Scott Sorensen, Eddie Davidsen

NEBRASKA
Good Life. Great Journey.
DEPARTMENT OF TRANSPORTATION

IHC SCOTT®

Outline

- Project overview
- Timeline of issue discovery and resolution
- Partnering best practices

Project Overview

- "L-62A North"
  - Part of Ports-to-Plains Alliance

Source: portstoplains.com

Project Overview

- “L-62A North”
  - Part of Ports-to-Plains Alliance
  - Connects “Alliance South” project w/ L-62A

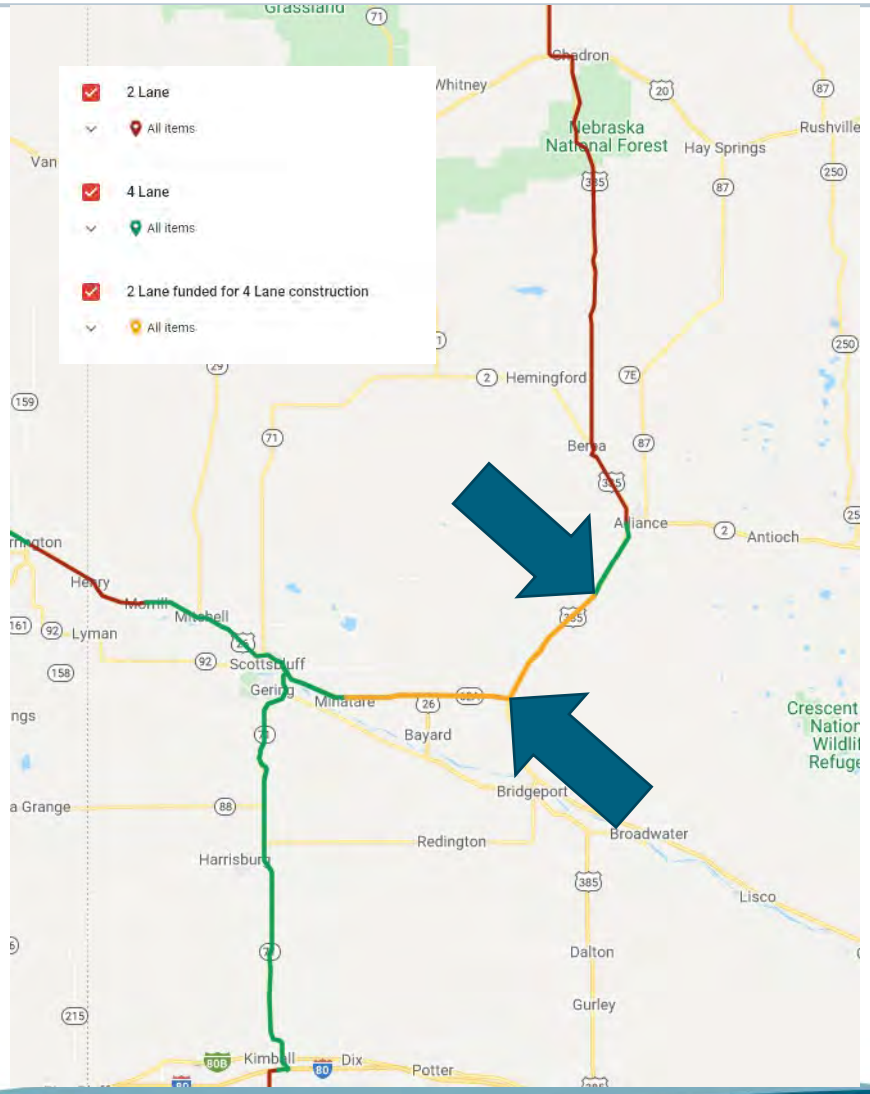

Source: heartlandexpressway.com

Project Overview

- "L-62A North"
  - Part of Ports-to-Plains Alliance
  - Connects "Alliance South" project w/ L-62A
  - 2 + 2 Strategy

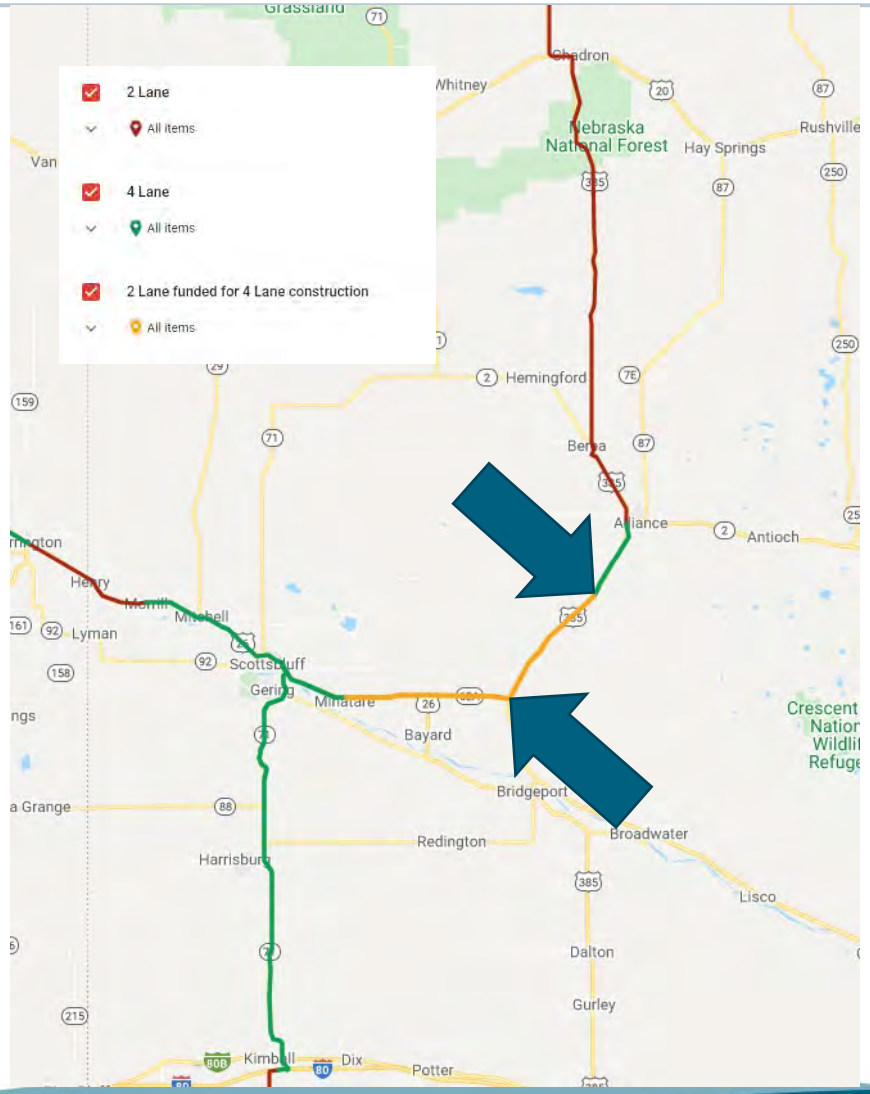

Source: heartlandexpressway.com

Project Overview

- "L-62A North"
  - Part of Ports-to-Plains Alliance
  - Connects "Alliance South" project w/ L-62A
  - 2 + 2 Strategy
  - 14.48 miles

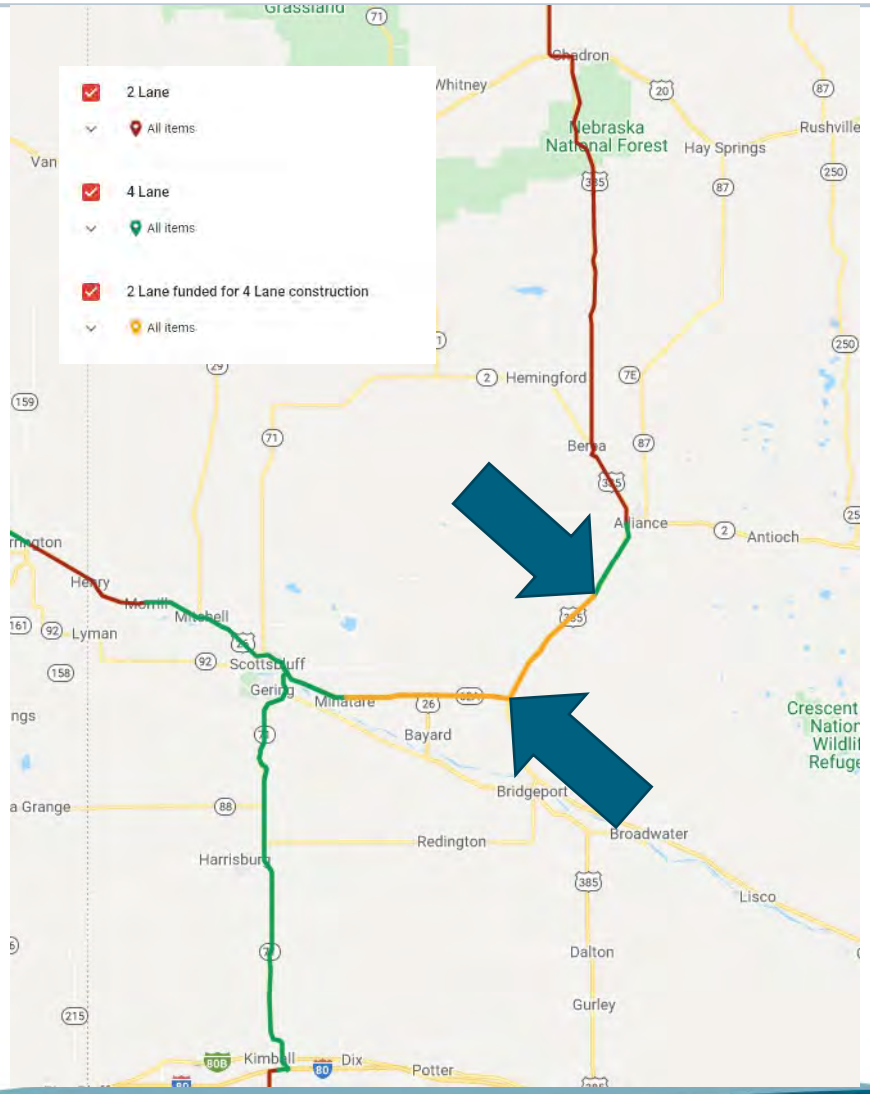

Source: heartlandexpressway.com

Project Overview

- "L-62A North"
  - Part of Ports-to-Plains Alliance
  - Connects "Alliance South" project w/ L-62A
  - 2 + 2 Strategy
  - 14.48 miles
  - $32 million

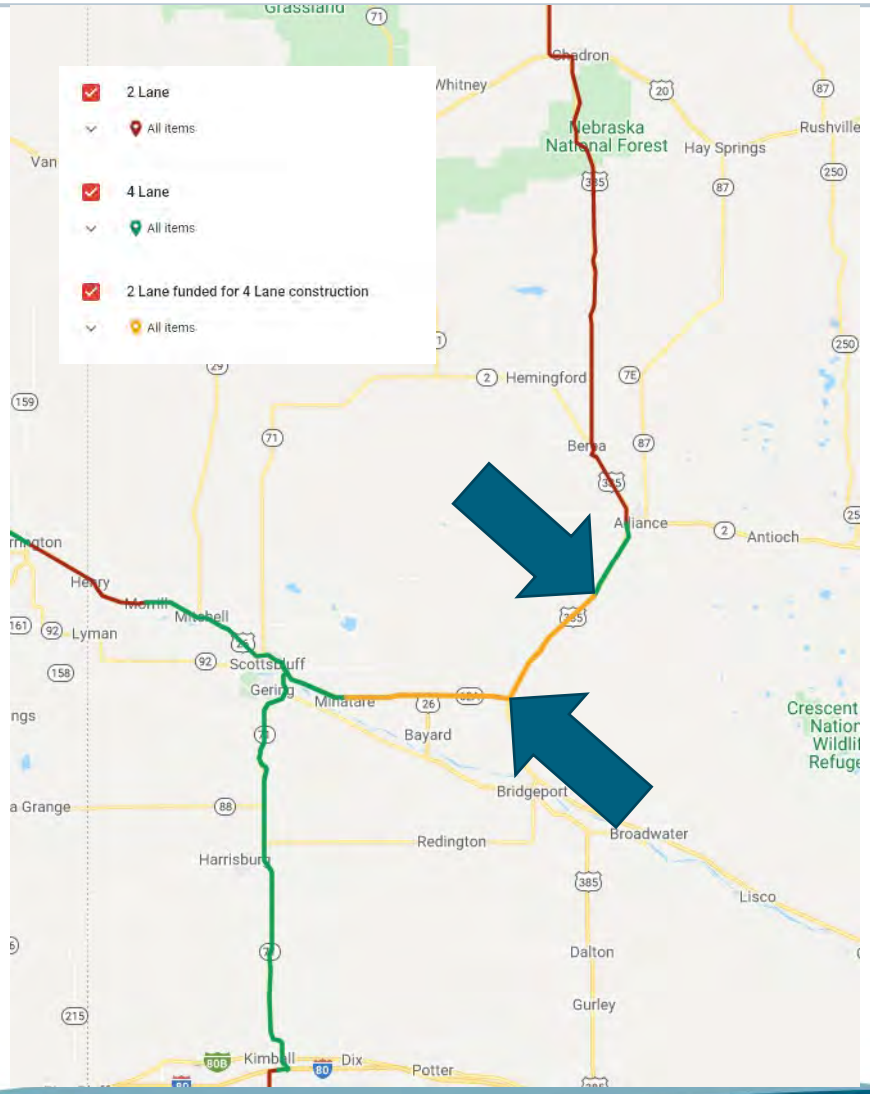

Source: heartlandexpressway.com

Project Overview

- "L-62A North"
  - Part of Ports-to-Plains Alliance
  - Connects "Alliance South" project w/ L-62A
  - 2 + 2 Strategy
  - 14.48 miles
  - $32 million
  - 1,059,550 CY of Excavation

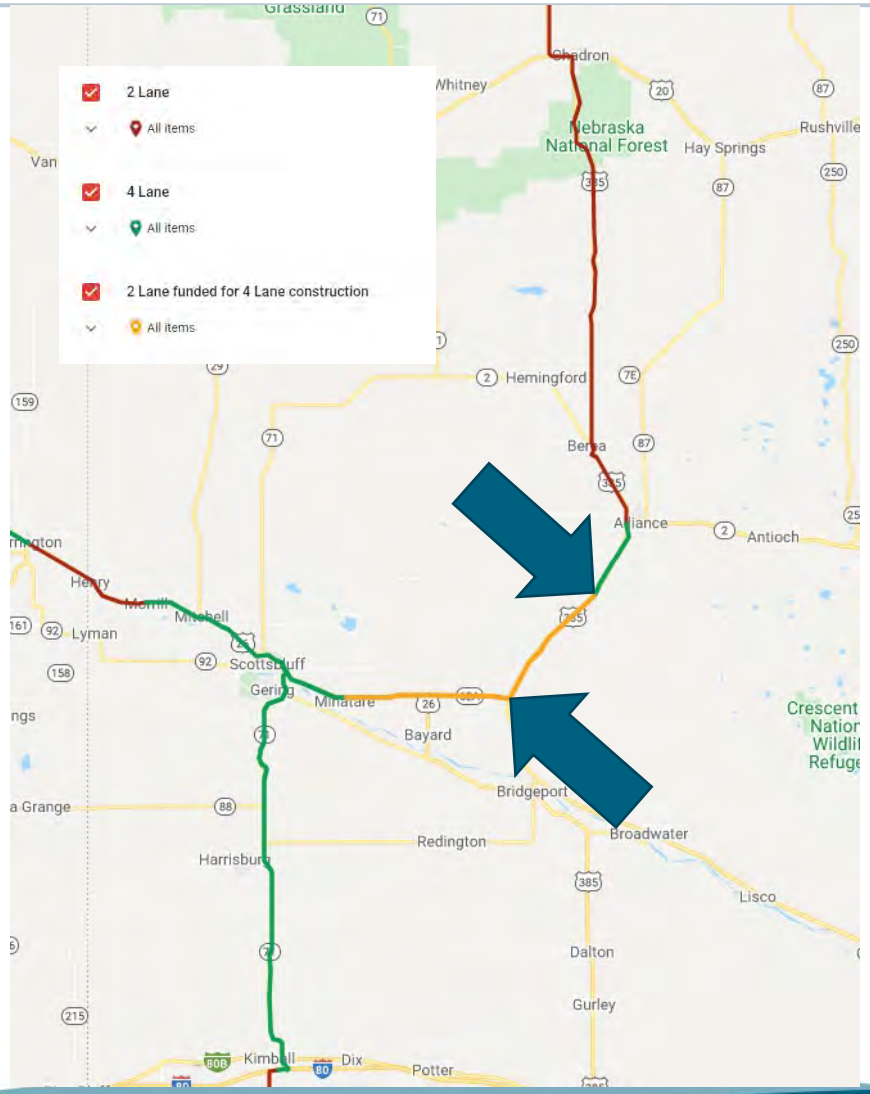

Source: heartlandexpressway.com

Project Overview

- "L-62A North"
  - Part of Ports-to-Plains Alliance
  - Connects "Alliance South" project w/ L-62A
  - 2 + 2 Strategy
  - 14.48 miles
  - $32 million
  - 1,059,550 CY of Excavation
  - Prime – IHC Scott
    - Grading Sub – Paul Reed Construction

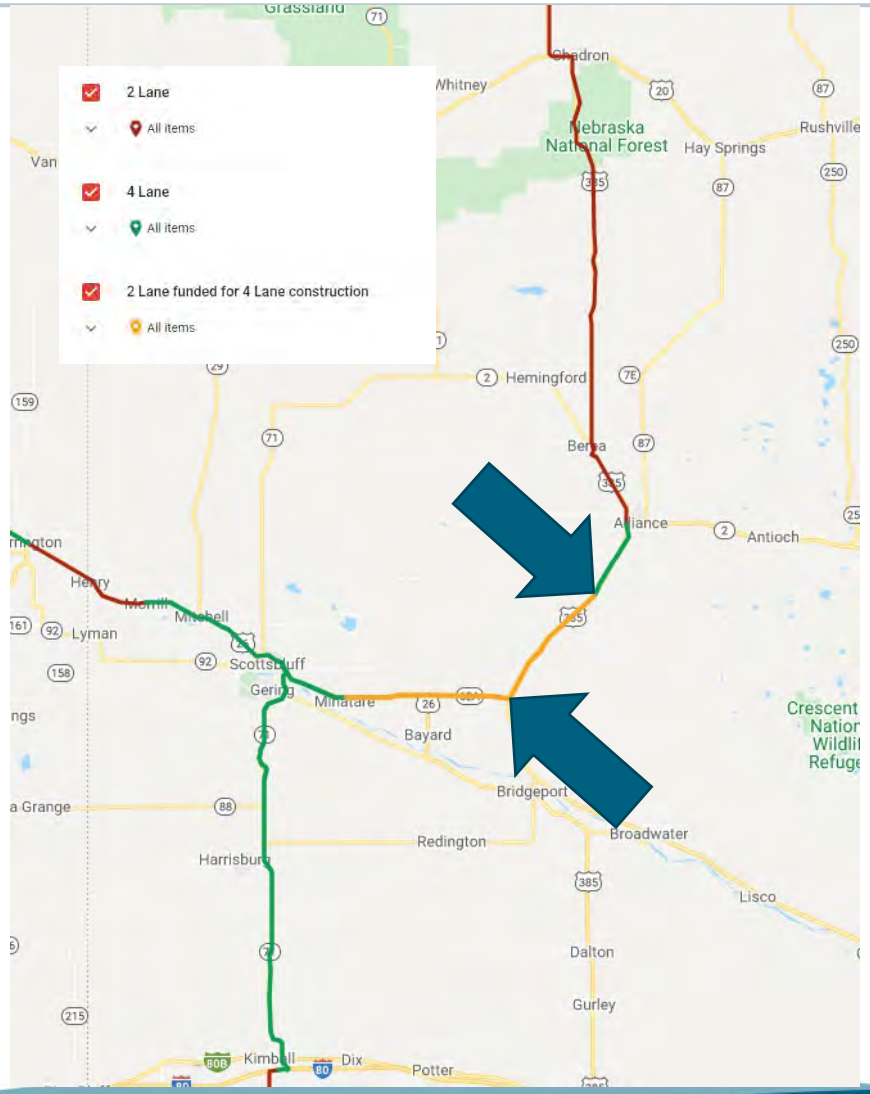

Source: heartlandexpressway.com

Project Overview

- "L-62A North"
  - Part of Ports-to-Plains Alliance
  - Connects "Alliance South" project w/ L-62A
  - 2 + 2 Strategy
  - 14.48 miles
  - $32 million
  - 1,059,550 CY of Excavation
  - Prime – IHC Scott
    - Grading Sub – Paul Reed Construction
  - Notice to Proceed on March 10, 2021

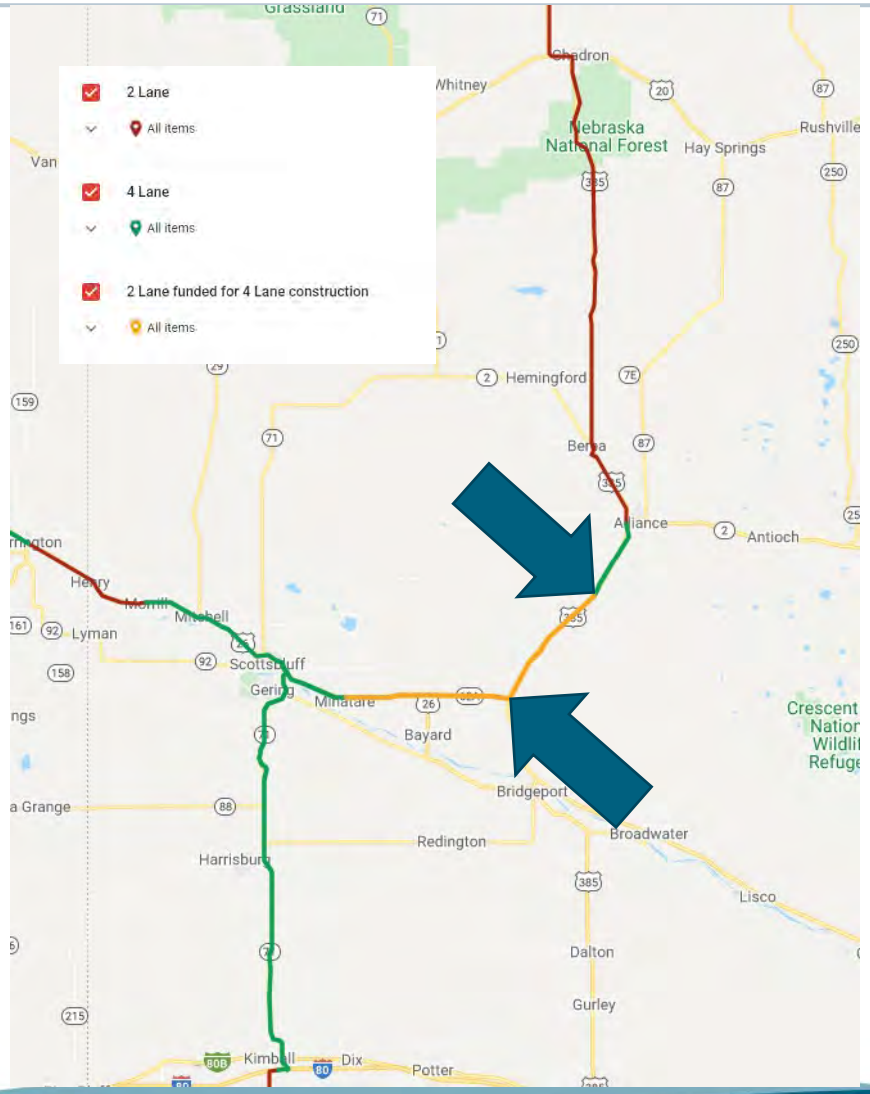

Source: heartlandexpressway.com

Issue discovery and resolution timeline

Unstable material discovered

March 30th

Issue discovery and resolution timeline

Unstable material discovered

March 30th

Issue discovery and resolution timeline

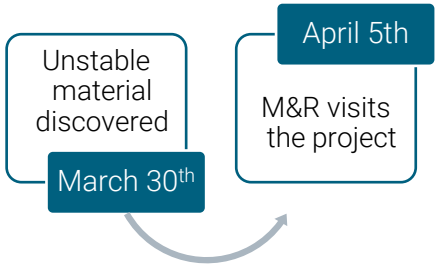

Issue discovery and resolution timeline

Unstable material discovered

March 30th

April 5th

M&R visits the project

Issue discovery and resolution timeline

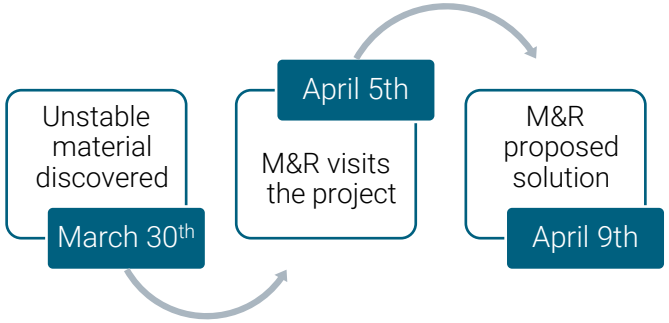

Issue discovery and resolution timeline

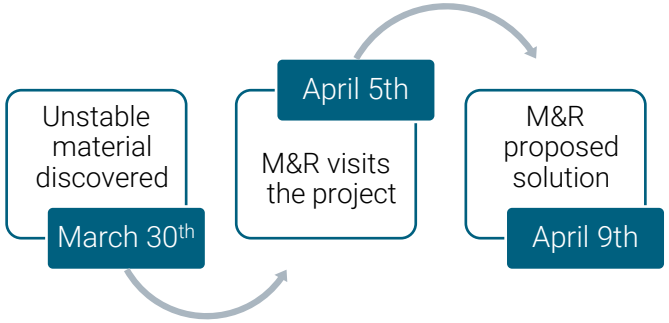

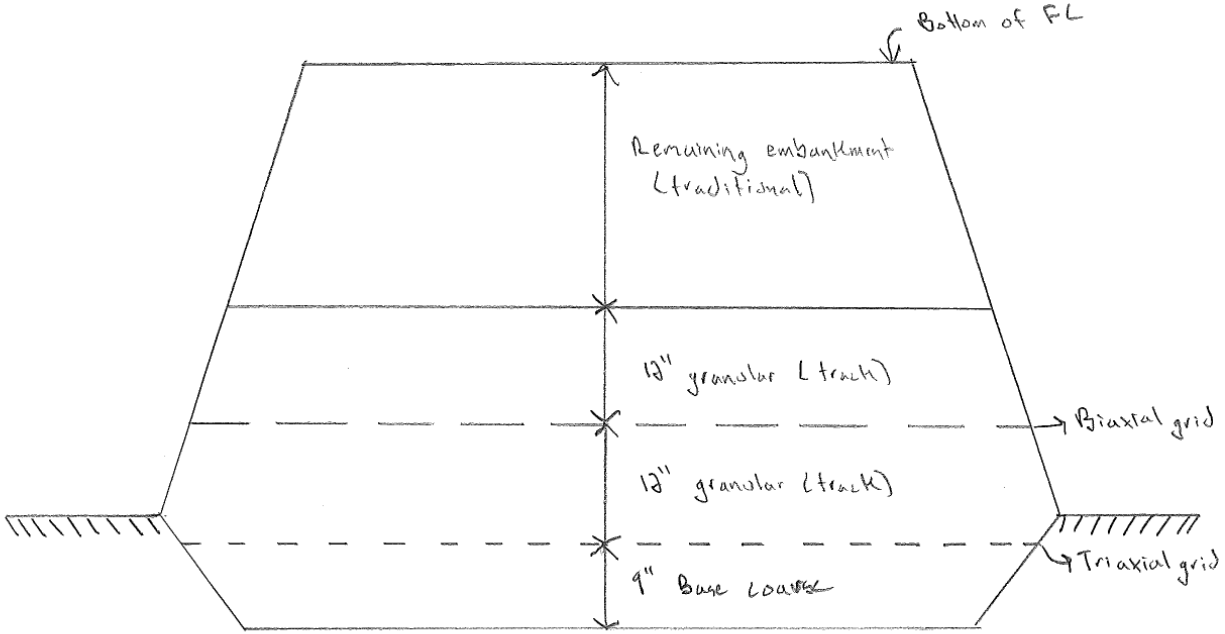

Issue discovery and resolution timeline

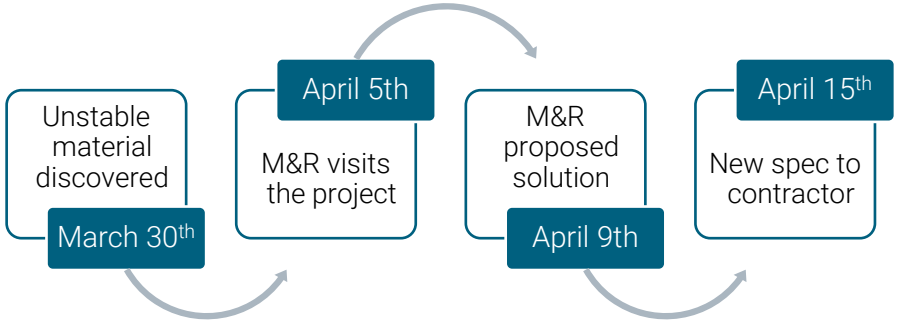

Issue discovery and resolution timeline

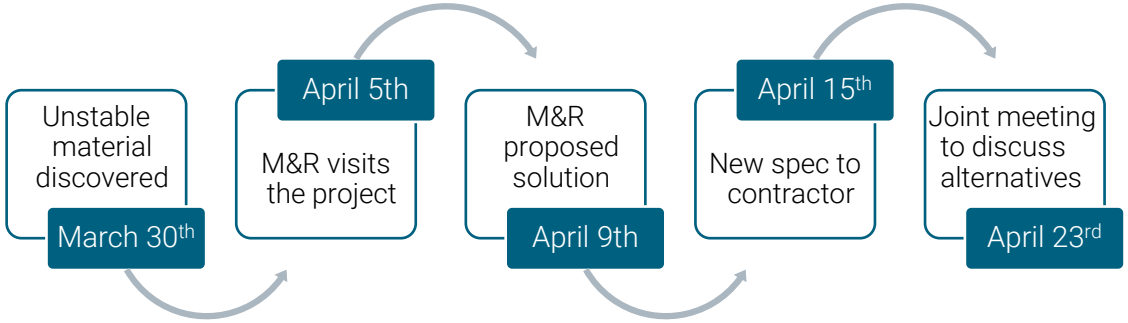

Issue discovery and resolution timeline

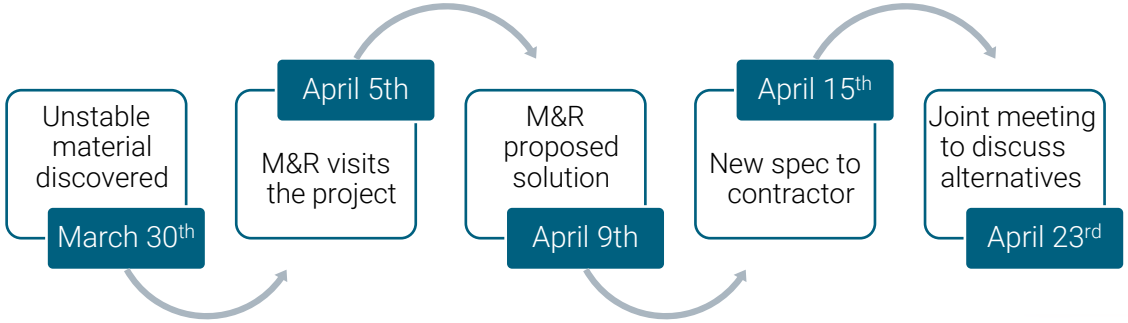

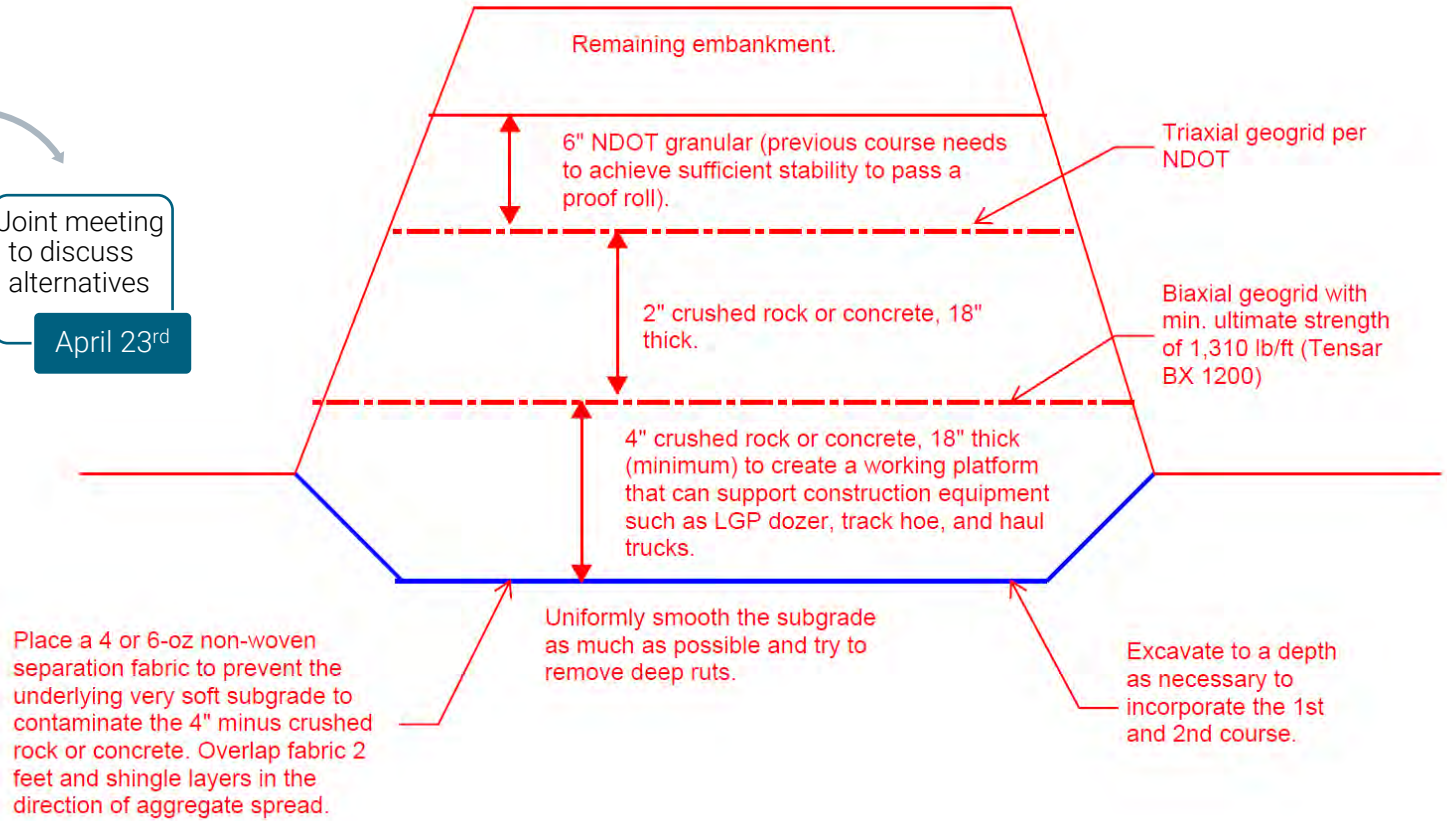

Issue discovery and resolution timeline

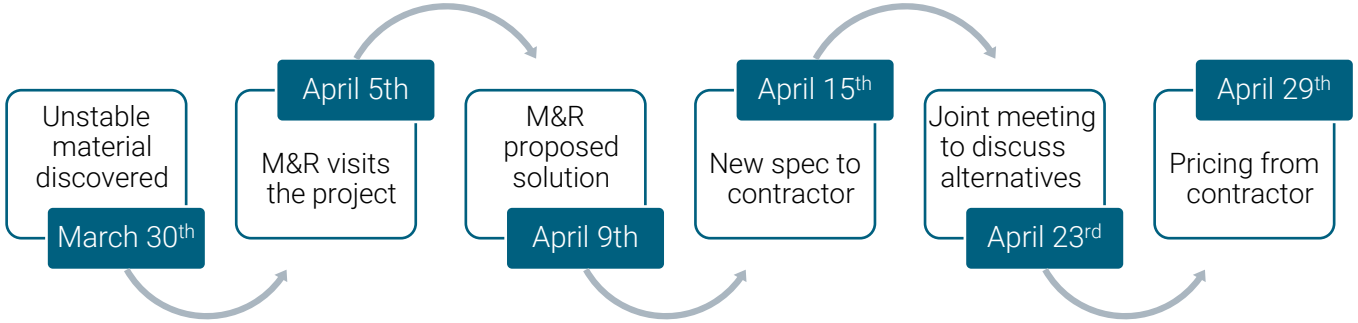

Issue discovery and resolution timeline

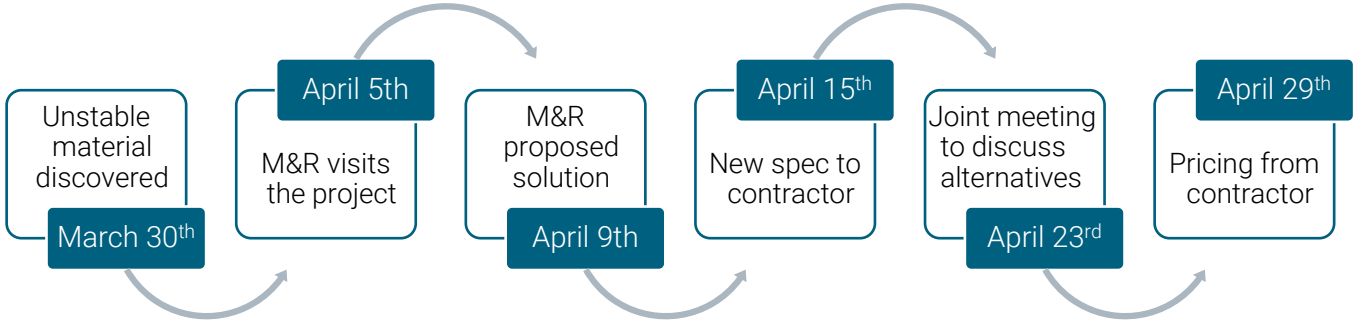

Tensar®

Issue discovery and resolution timeline

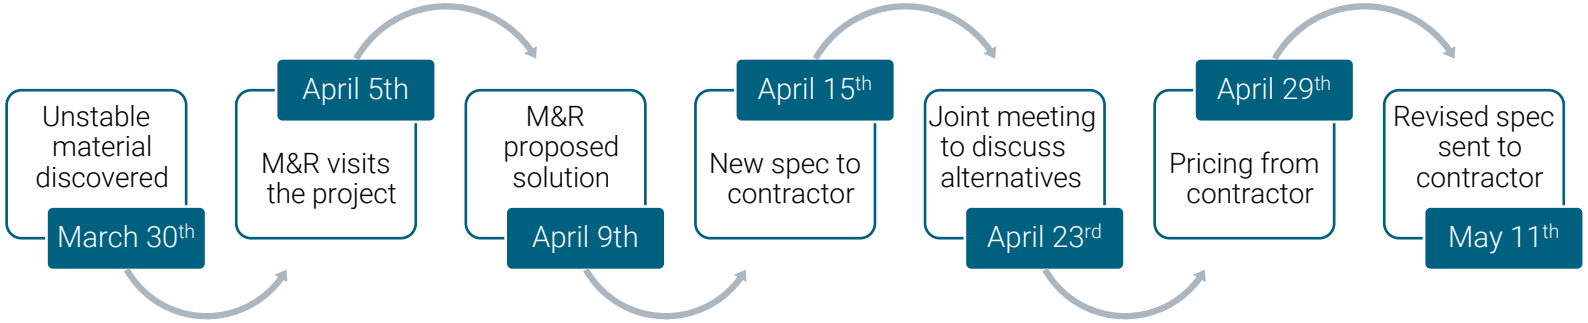

Issue discovery and resolution timeline

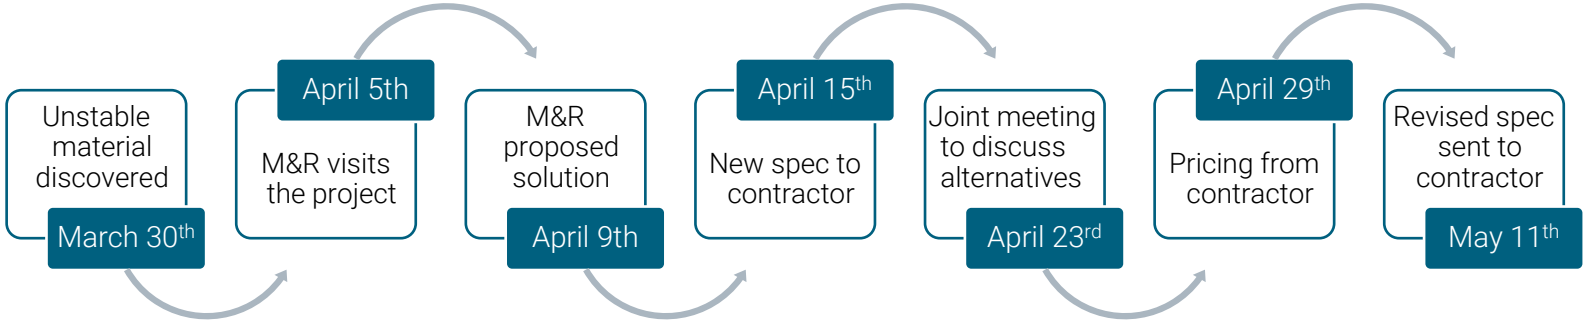

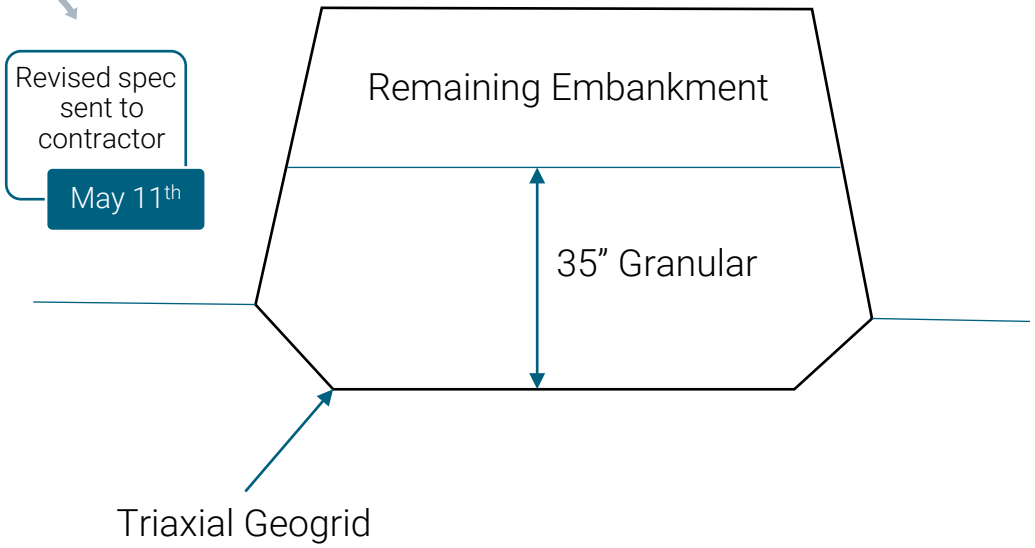

Issue discovery and resolution timeline

Issue discovery and resolution timeline

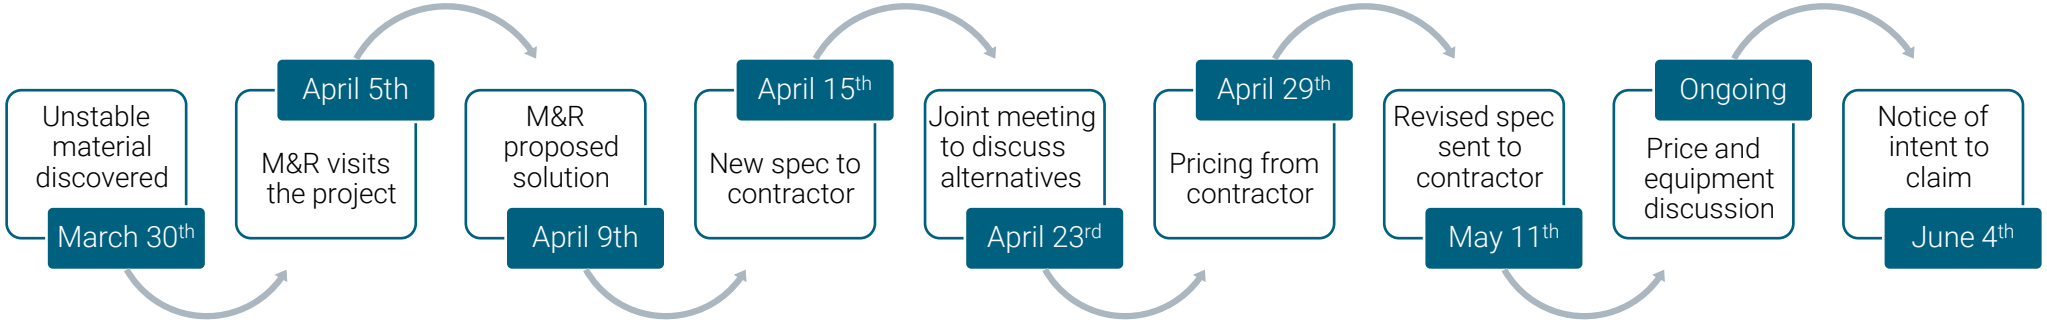

Issue discovery and resolution timeline

Issue discovery and resolution timeline

June 18th

Contractor begins extra work

Issue discovery and resolution timeline

June 18th

Contractor begins extra work

Issue discovery and resolution timeline

June 18th

Contractor begins extra work

How to be good partners

- Communication is <u>KEY</u>
- Identify risks and rewards of stakeholders
- Avoid adversarial relationships

How to be good partners

- Communication is <u>KEY</u>
- Identify risks and rewards of stakeholders
- Avoid adversarial relationships

How to be good partners

- Communication is <u>KEY</u>
- Identify risks and rewards of stakeholders
- Avoid adversarial relationships
- Manage perceptions
- Look for “win-win” opportunities
- Employ deadlocking countermeasures
- Implement solution

Thank you
